Probability of Success

AIM Home Page

Mr. Edmund Blackford's Portal - PM UH
Acquisition Information Management (AIM v6.8)
Home
AIM Info
Apps
Meta Data
Documents
Contact Aim
Help and Faq
My AIM
Logout
AIM 6.8 Release Notes
Latest News at AI TESS
March 2004 DEAS data loaded (04/12/2004)
Probability of Program Success Released (01/09/2004)
Acquisition Links A-Z
Acquisition
OSD for Acquisition, Technolgy, and Logistics
Acquisition Reform Network
Assistant Secretary of the Army for Acquisition, Logistics, and Technology
PEO PM Listing
U.S. Army Acquisition Support Center (ASC)
U.S. Army Acquisition Logistics and Technology Enterprise Systems and Services (ALTESS)
Consolidated Acquisition Reporting System (CARS)
Department of Army
Army Homepage
U.S. Army Materiel Command
Army Knowledge Online (AKO)
Army Recapitalization Management
Army Test and Evaluation Command
ATEC Decision Support System (ADSS)
Army Test and Evaluation Command (ATEC) Home
Career
Army Training Requirements and Resources System
Army Acquisition Corp
Congressional
Thomas Legislative Information on the Internet
Event Calendar
Apr -May 2004
Su Mo Tu We Th Fr Sa
25 26 27 28 29 30 1
2 3 4 5 6 7 8
9 10 11 12 13 14 15
16 17 18 19 20 21 22
Upcoming Events
Apr 27 29
Acquisition Enterprise User Group Conference
View Calendar
Commander's Corner
LTC Fernando L. Torrent
We are pleased to announce that the Acquisition Enterprise User Group Conference will be held at the Renaissance Portsmouth Hotel & Waterfront Conference Center in Portsmouth, Virginia, 27-29 April 2004 [continued]
Acquisition Publications
AIM ACAT Reports
2004 Congressional Marks Report
Annual Defense Report 2001
Army AI &T Magazine
Army Logistician
U.S. Army Publishing Agency

AIM Contact Page

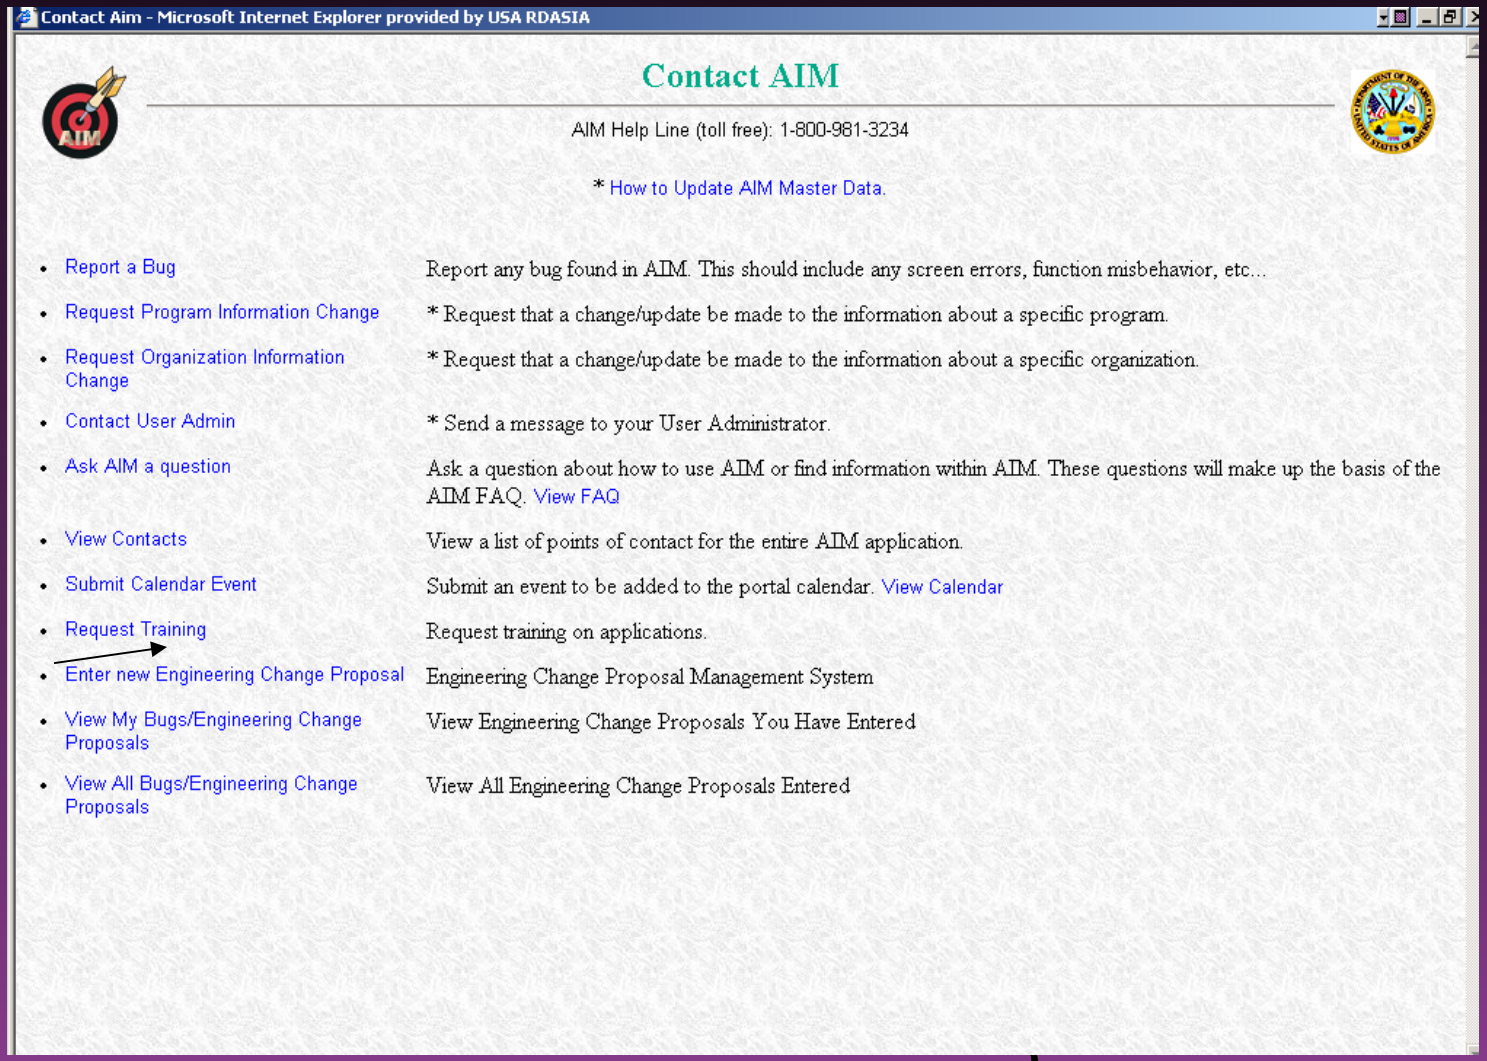
Contact Aim - Microsoft Internet Explorer provided by USA RDASIA
Contact AIM
AIM Help Line (toll free): 1-800-981-3234
* How to Update AIM Master Data.
Report a Bug
Report any bug found in AIM. This should include any screen errors, function misbehavior, etc...
Request Program Information Change
* Request that a change/update be made to the information about a specific program.
Request Organization Information Change
* Request that a change/update be made to the information about a specific organization.
Contact User Admin
* Send a message to your User Administrator.
Ask AIM a question
Ask a question about how to use AIM or find information within AIM. These questions will make up the basis of the AIM FAQ. View FAQ
View Contacts
View a list of points of contact for the entire AIM application.
Submit Calendar Event
Submit an event to be added to the portal calendar. View Calendar
Request Training
Request training on applications.
Enter new Engineering Change Proposal
Engineering Change Proposal Management System
View My Bugs/Engineering Change Proposals
View Engineering Change Proposals You Have Entered
View All Bugs/Engineering Change Proposals
View All Engineering Change Proposals Entered

Select to request training

AIM Help and FAQ

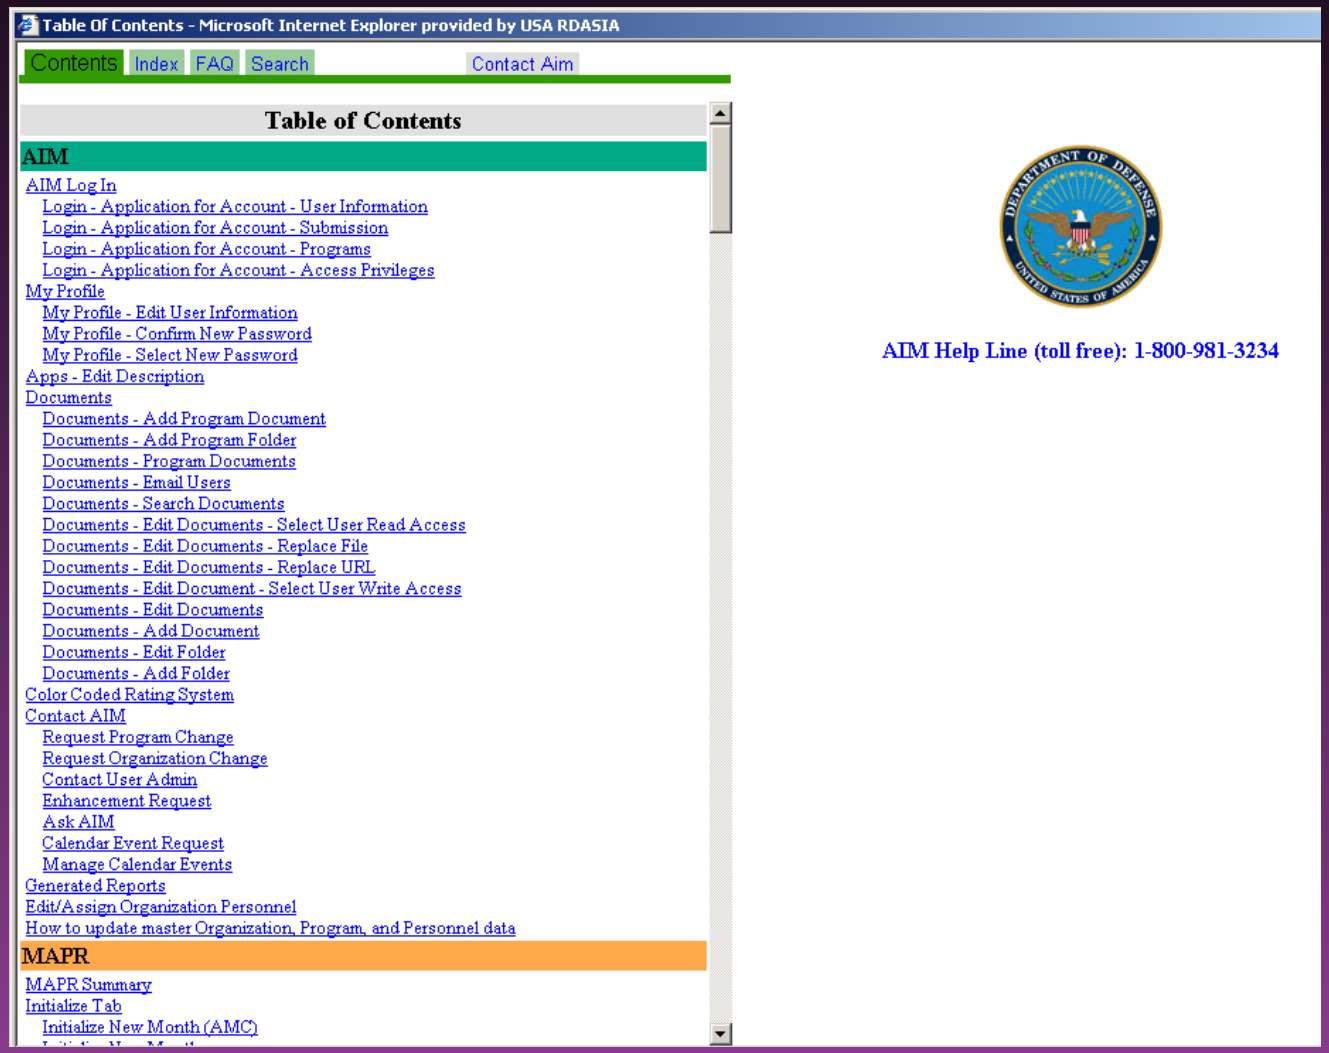
Table Of Contents - Microsoft Internet Explorer provided by USA RDASIA
Contents
Index
FAQ
Search
Contact Aim
Table of Contents
AIM
AIM Log In
Login - Application for Account - User Information
Login - Application for Account - Submission
Login - Application for Account - Programs
Login - Application for Account - Access Privileges
My Profile
My Profile - Edit User Information
My Profile - Confirm New Password
My Profile - Select New Password
Apps - Edit Description
Documents
Documents - Add Program Document
Documents - Add Program Folder
Documents - Program Documents
Documents - Email Users
Documents - Search Documents
Documents - Edit Documents - Select User Read Access
Documents - Edit Documents - Replace File
Documents - Edit Documents - Replace URL
Documents - Edit Document - Select User Write Access
Documents - Edit Documents
Documents - Add Document
Documents - Edit Folder
Documents - Add Folder
Color Coded Rating System
Contact AIM
Request Program Change
Request Organization Change
Contact User Admin
Enhancement Request
Ask AIM
Calendar Event Request
Manage Calendar Events
Generated Reports
Edit/Assign Organization Personnel
How to update master Organization, Program, and Personnel data
MAPR
MAPR Summary
Initialize Tab
Initialize New Month (AMC)
AIM Help Line (toll free): 1-800-981-3234

AIM ‘My AIM’

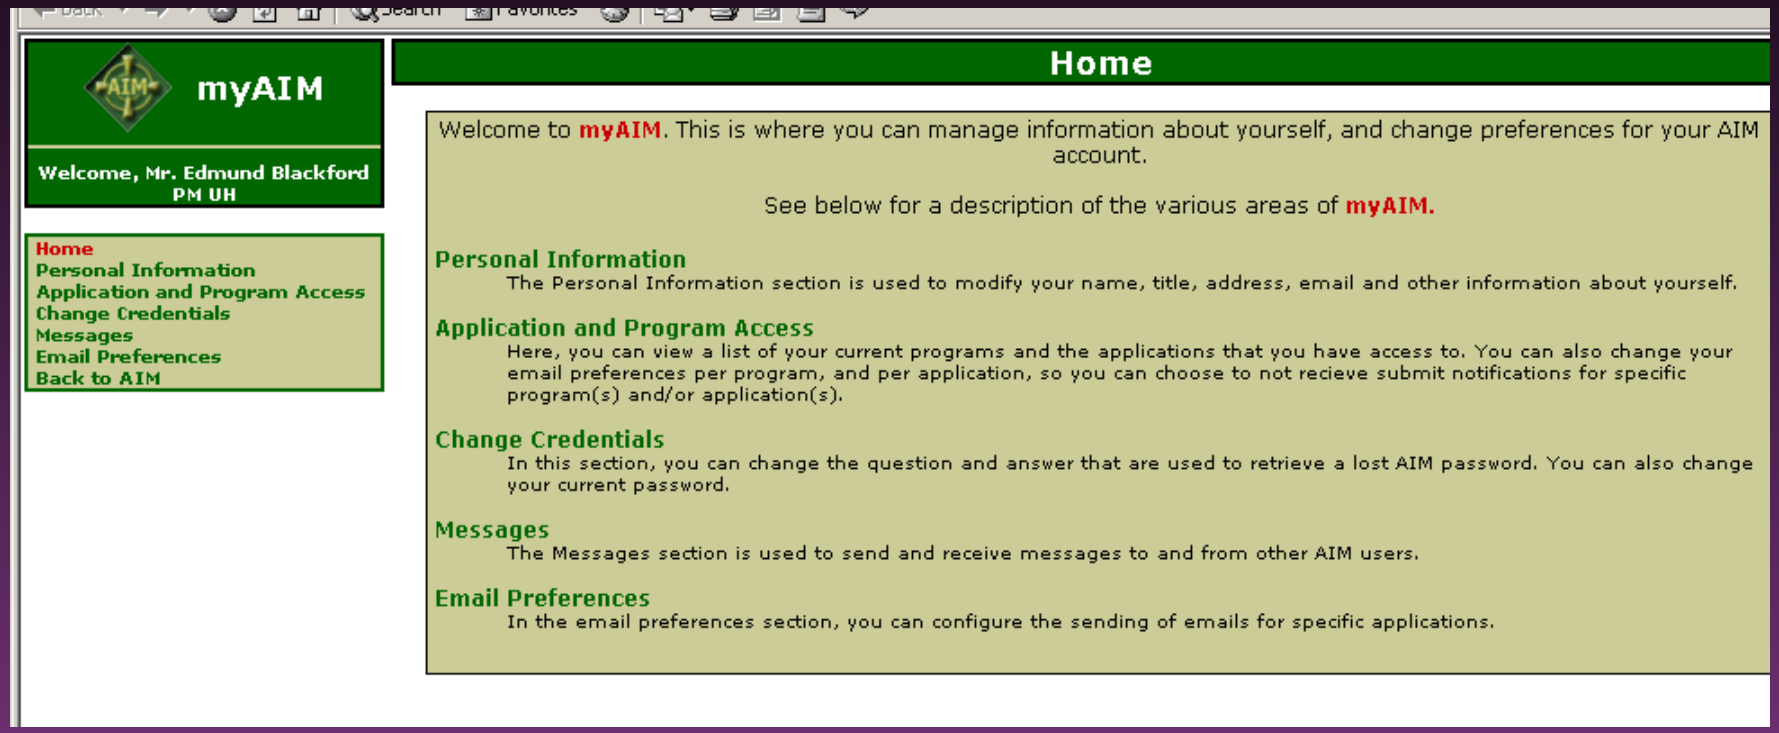
myAIM
Welcome, Mr. Edmund Blackford
PM UH
Home
Personal Information
Application and Program Access
Change Credentials
Messages
Email Preferences
Back to AIM
Home
Welcome to myAIM. This is where you can manage information about yourself, and change preferences for your AIM account.
See below for a description of the various areas of myAIM.
Personal Information
The Personal Information section is used to modify your name, title, address, email and other information about yourself.
Application and Program Access
Here, you can view a list of your current programs and the applications that you have access to. You can also change your email preferences per program, and per application, so you can choose to not recieve submit notifications for specific program(s) and/or application(s).
Change Credentials
In this section, you can change the question and answer that are used to retrieve a lost AIM password. You can also change your current password.
Messages
The Messages section is used to send and receive messages to and from other AIM users.
Email Preferences
In the email preferences section, you can configure the sending of emails for specific applications.

AIM Release Notes

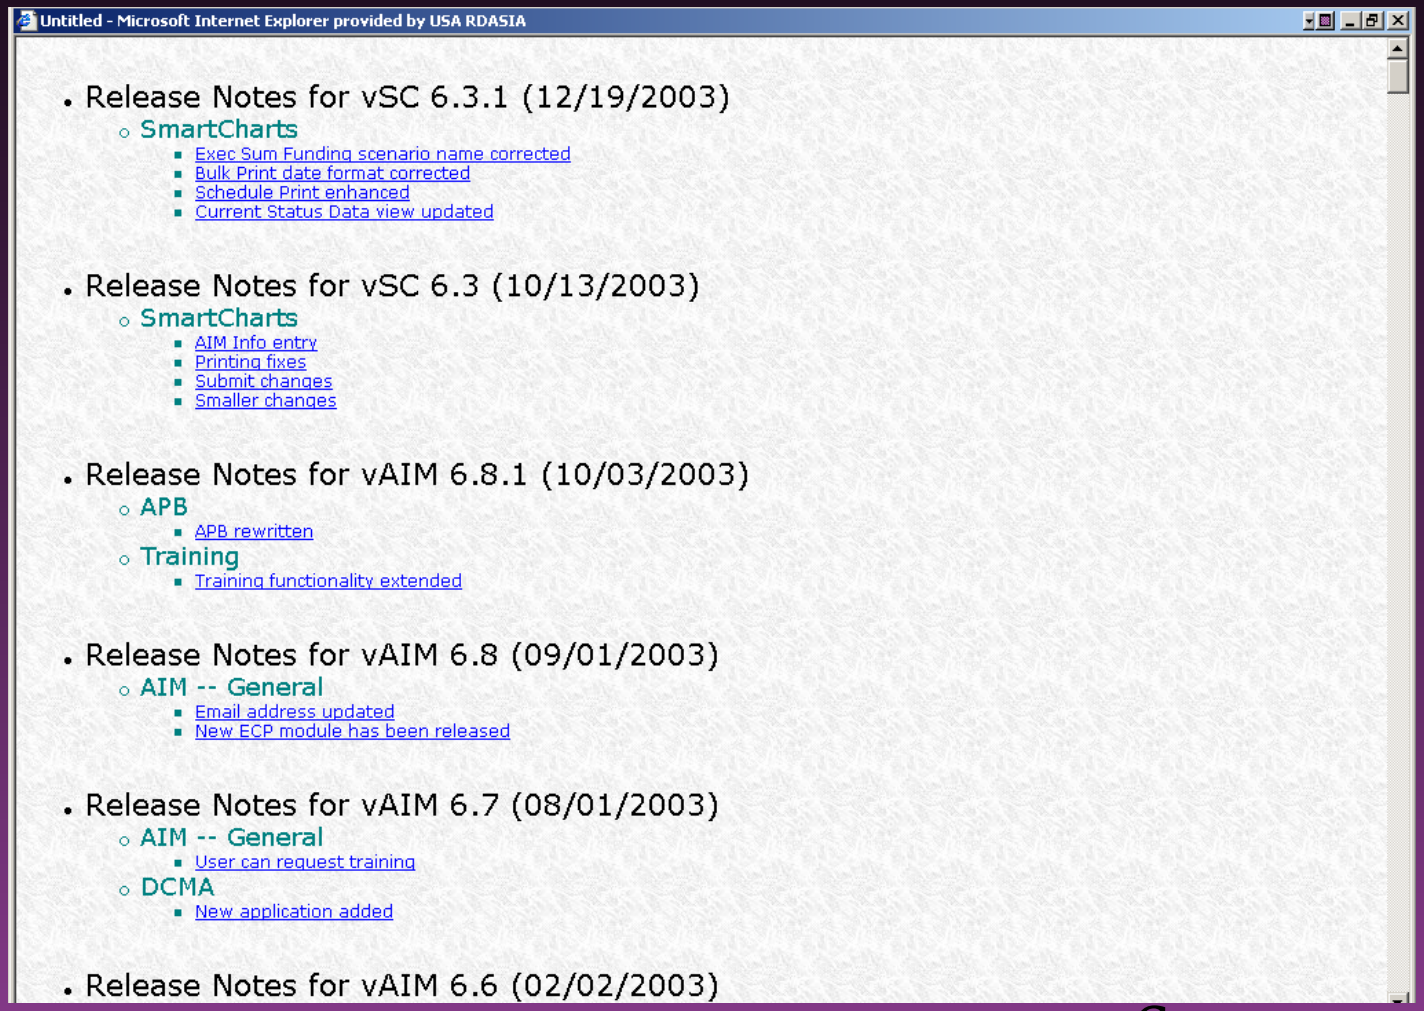

AIM Release Notes

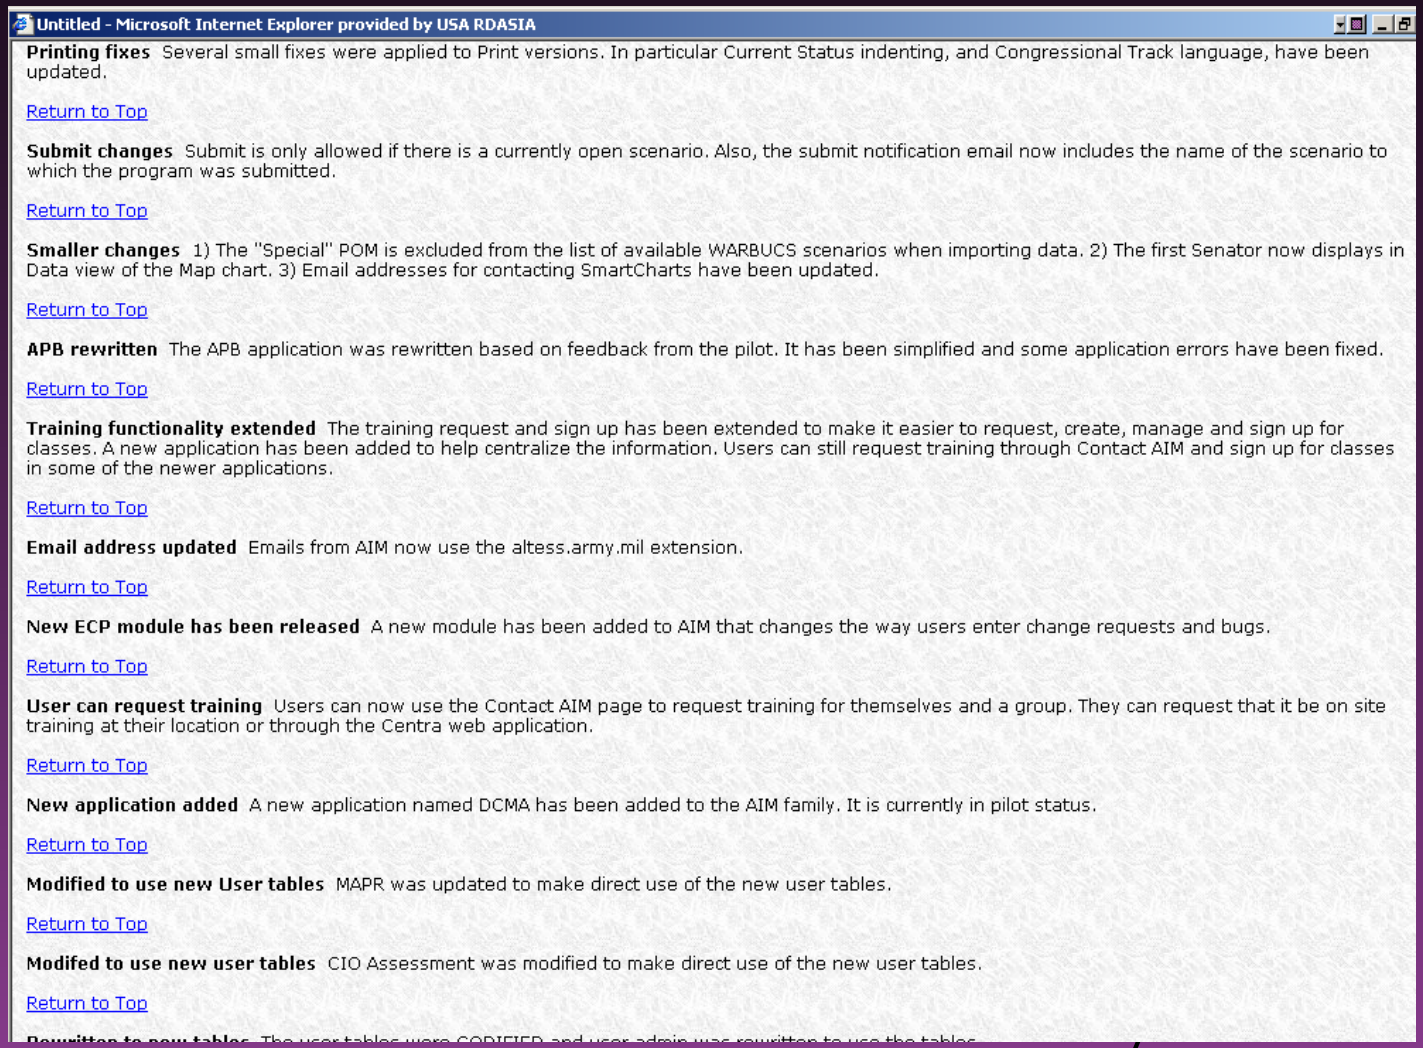
Untitled - Microsoft Internet Explorer provided by USA RDASIA
Printing fixes Several small fixes were applied to Print versions. In particular Current Status indenting, and Congressional Track language, have been updated.
Return to Top
Submit changes Submit is only allowed if there is a currently open scenario. Also, the submit notification email now includes the name of the scenario to which the program was submitted.
Return to Top
Smaller changes 1) The "Special" POM is excluded from the list of available WARBUCS scenarios when importing data. 2) The first Senator now displays in Data view of the Map chart. 3) Email addresses for contacting SmartCharts have been updated.
Return to Top
APB rewritten The APB application was rewritten based on feedback from the pilot. It has been simplified and some application errors have been fixed.
Return to Top
Training functionality extended The training request and sign up has been extended to make it easier to request, create, manage and sign up for classes. A new application has been added to help centralize the information. Users can still request training through Contact AIM and sign up for classes in some of the newer applications.
Return to Top
Email address updated Emails from AIM now use the altess.army.mil extension.
Return to Top
New ECP module has been released A new module has been added to AIM that changes the way users enter change requests and bugs.
Return to Top
User can request training Users can now use the Contact AIM page to request training for themselves and a group. They can request that it be on site training at their location or through the Centra web application.
Return to Top
New application added A new application named DCMA has been added to the AIM family. It is currently in pilot status.
Return to Top
Modified to use new User tables MAPR was updated to make direct use of the new user tables.
Return to Top
Modifed to use new user tables CIO Assessment was modified to make direct use of the new user tables.
Return to Top

AIM Applications Tabs

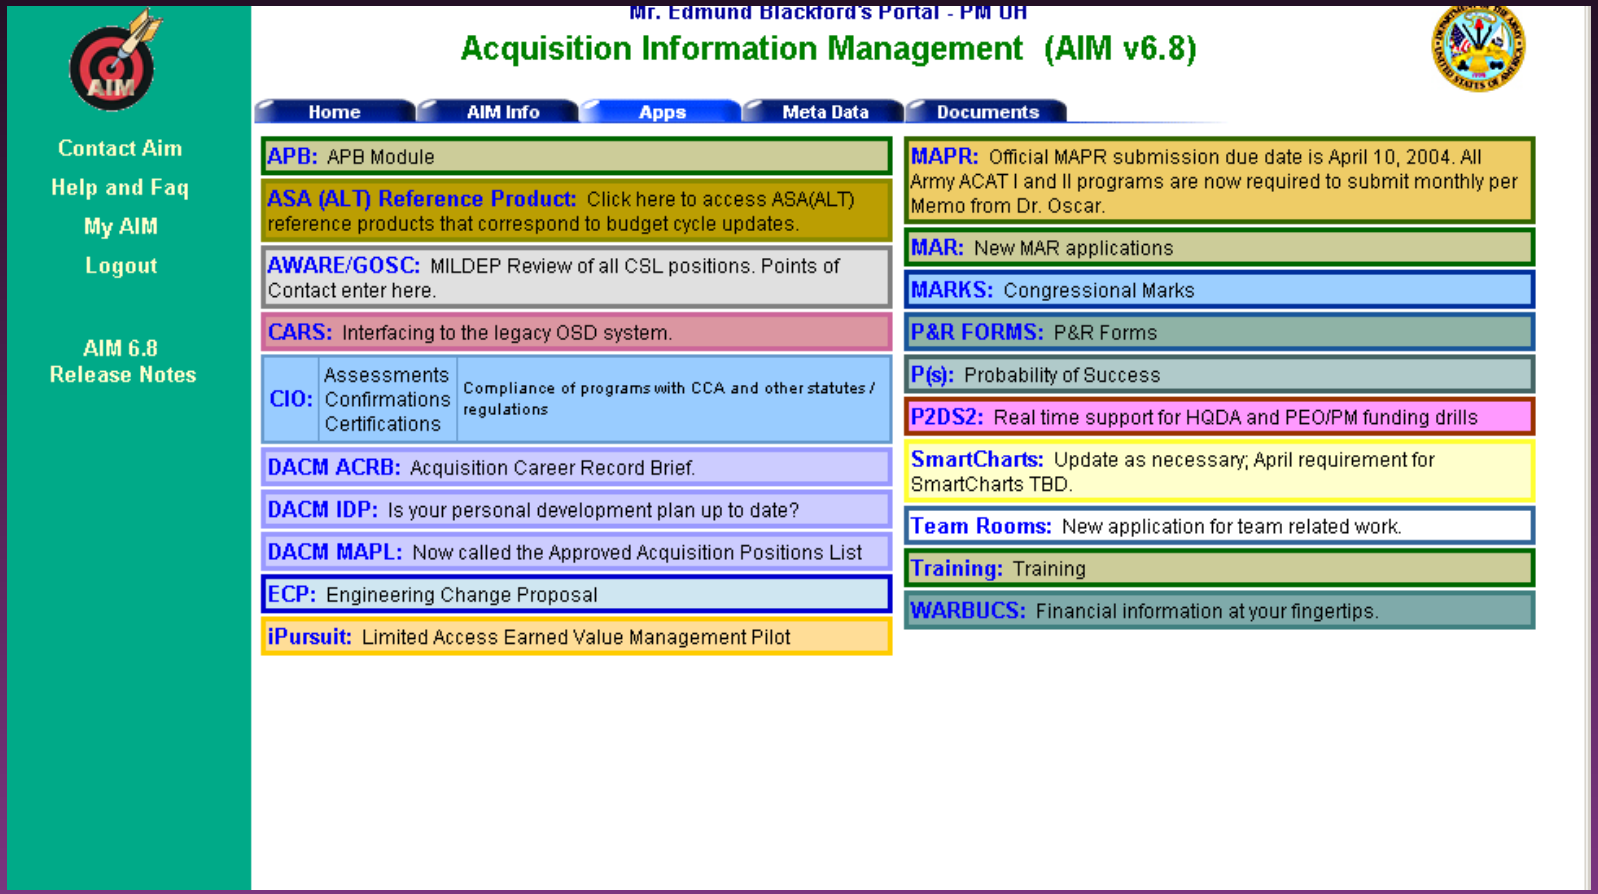
Contact Aim
Help and Faq
My AIM
Logout
AIM 6.8
Release Notes
Mr. Edmund Blackford's Portal - PM UH
Acquisition Information Management (AIM v6.8)
Home
AIM Info
Apps
Meta Data
Documents
APB: APB Module
ASA (ALT) Reference Product: Click here to access ASA(ALT) reference products that correspond to budget cycle updates.
AWARE/GOSC: MILDEP Review of all CSL positions. Points of Contact enter here.
CARS: Interfacing to the legacy OSD system.
CIO: Assessments Confirmations Certifications
Compliance of programs with CCA and other statutes / regulations
DACM ACRB: Acquisition Career Record Brief.
DACM IDP: Is your personal development plan up to date?
DACM MAPL: Now called the Approved Acquisition Positions List
ECP: Engineering Change Proposal
iPursuit: Limited Access Earned Value Management Pilot
MAPR: Official MAPR submission due date is April 10, 2004. All Army ACAT I and II programs are now required to submit monthly per Memo from Dr. Oscar.
MAR: New MAR applications
MARKS: Congressional Marks
P&R FORMS: P&R Forms
P(s): Probability of Success
P2DS2: Real time support for HQDA and PEO/PM funding drills
SmartCharts: Update as necessary; April requirement for SmartCharts TBD.
Team Rooms: New application for team related work.
Training: Training
WARBUCS: Financial information at your fingertips.

P(S) Homepage

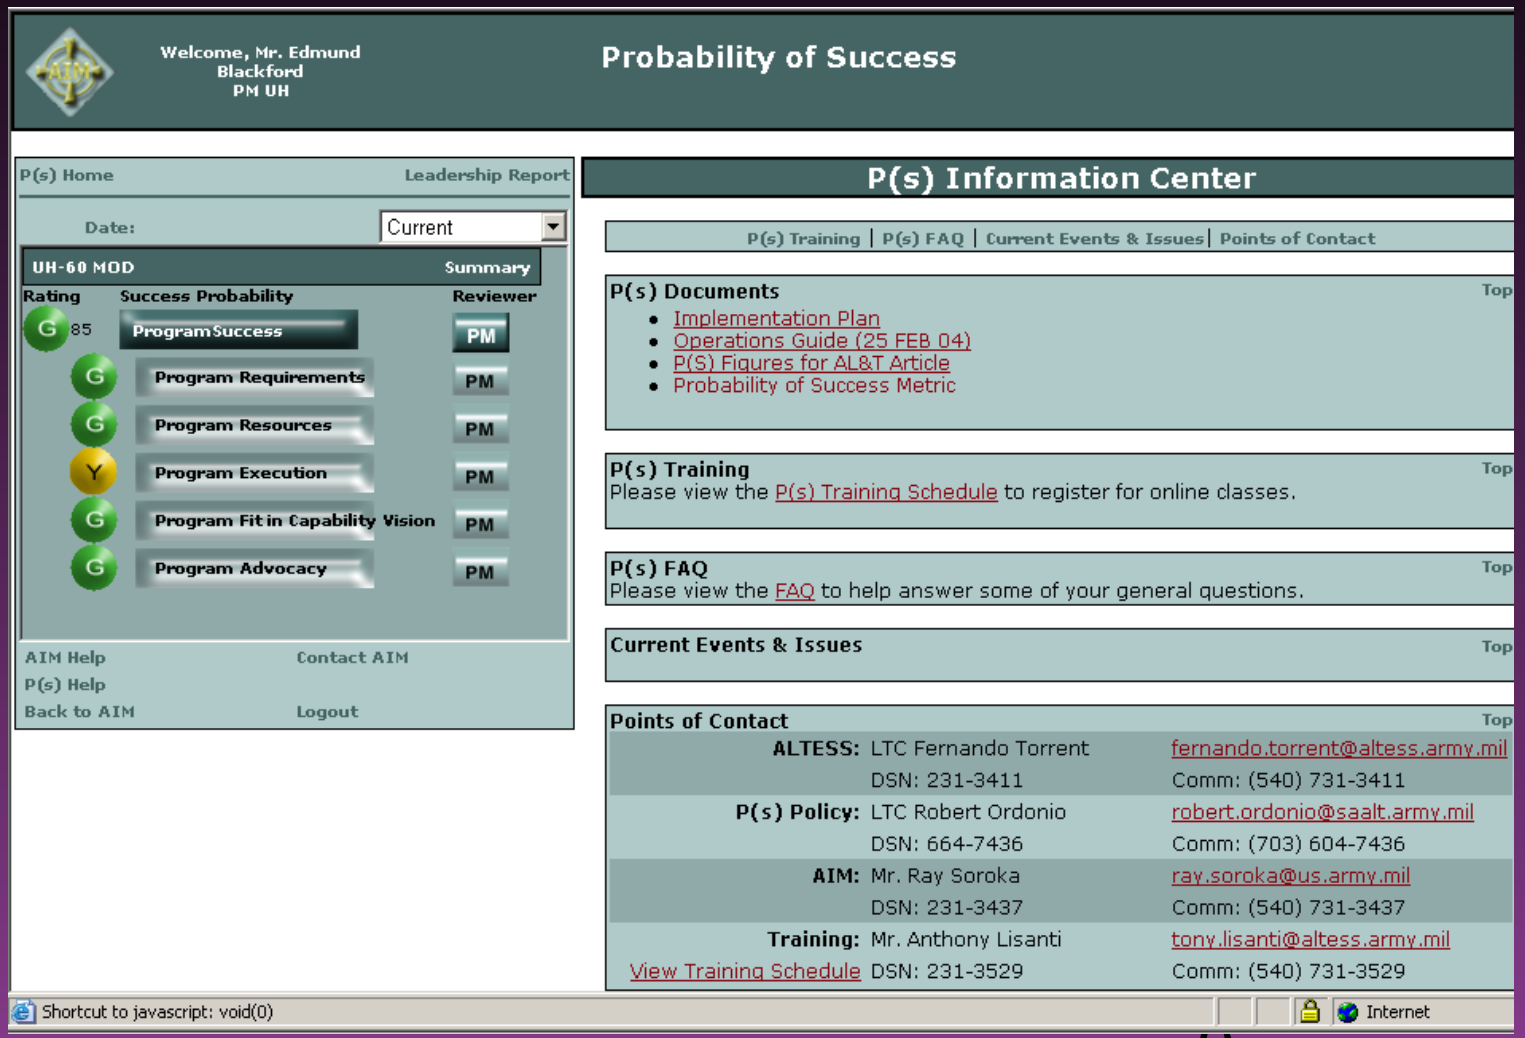
Welcome, Mr. Edmund Blackford
PM UH
Probability of Success
P(s) Home
Leadership Report
Date:
Current
UH-60 MOD
Summary
Rating
Success Probability
Reviewer
85
ProgramSuccess
PM
Program Requirements
Program Resources
Program Execution
Program Fit in Capability Vision
Program Advocacy
AIM Help
Contact AIM
P(s) Help
Back to AIM
Logout
P(s) Information Center
P(s) Training | P(s) FAQ | Current Events & Issues | Points of Contact
P(s) Documents
Top
Implementation Plan
Operations Guide (25 FEB 04)
P(S) Figures for AL&T Article
Probability of Success Metric
P(s) Training
Please view the P(s) Training Schedule to register for online classes.
P(s) FAQ
Please view the FAQ to help answer some of your general questions.
Current Events & Issues
Points of Contact
ALTESS: LTC Fernando Torrent fernando.torrent@altess.army.mil
DSN: 231-3411 Comm: (540) 731-3411
P(s) Policy: LTC Robert Ordonio robert.ordonio@saalt.army.mil
DSN: 664-7436 Comm: (703) 604-7436
AIM: Mr. Ray Soroka ray.soroka@us.army.mil
DSN: 231-3437 Comm: (540) 731-3437
Training: Mr. Anthony Lisanti tony.lisanti@altess.army.mil
View Training Schedule DSN: 231-3529 Comm: (540) 731-3529
Shortcut to javascript: void(0)
Internet

P(S) Information Center

Newest Version of Operations Guide

View Online training

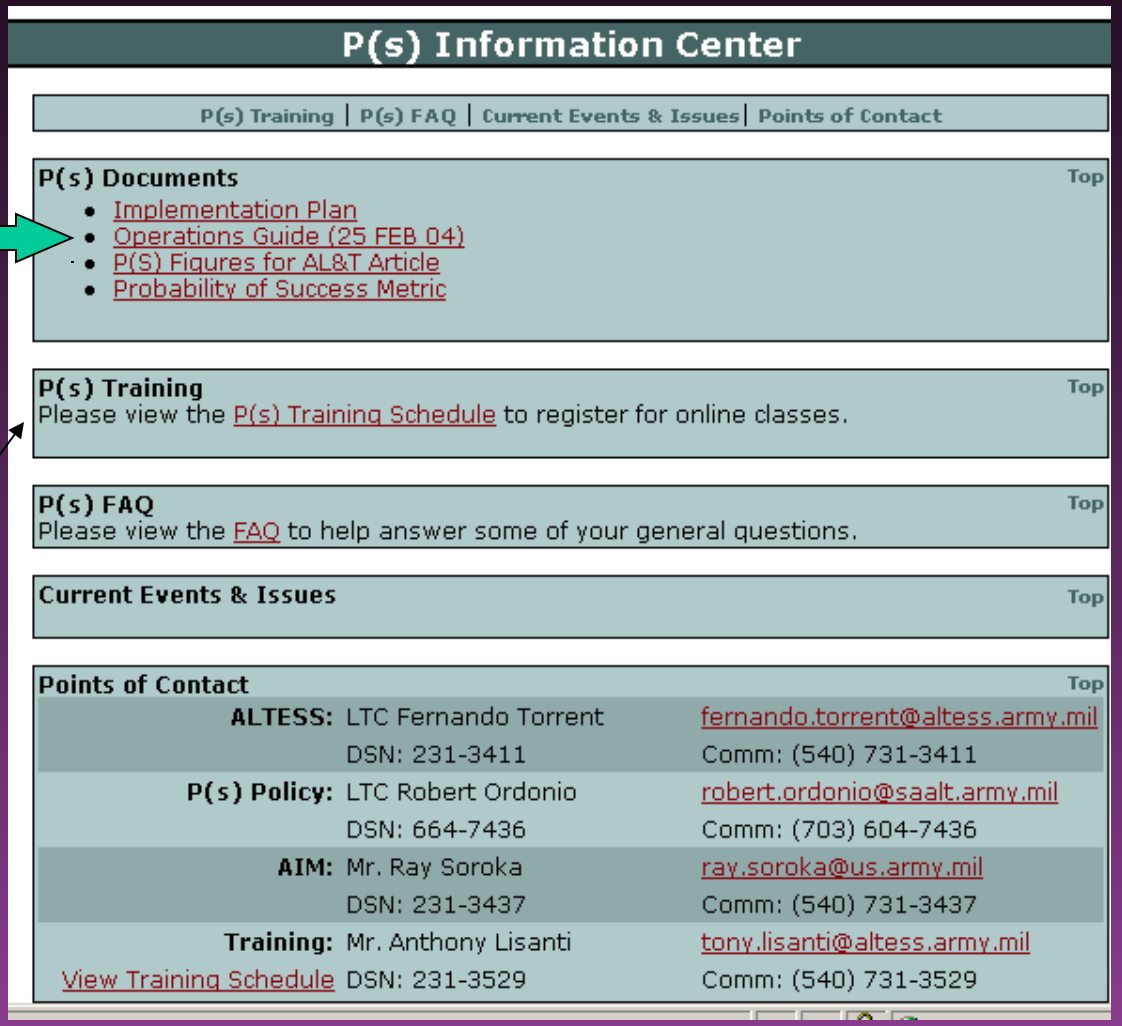

P(s) Information Center

P(s) Training | P(s) FAQ | Current Events & Issues | Points of Contact

P(s) Documents Top

- Implementation Plan
- Operations Guide (25 FEB 04)
- P(S) Figures for AL&T Article
- Probability of Success Metric

P(s) Training Top

Please view the P(s) Training Schedule to register for online classes.

P(s) FAQ Top

Please view the FAQ to help answer some of your general questions.

Current Events & Issues Top

Points of Contact Top

ALTESS:	LTC Fernando Torrent	fernando.torrent@altess.army.mil
	DSN: 231-3411	Comm: (540) 731-3411
P(s) Policy:	LTC Robert Ordonio	robert.ordonio@saalt.army.mil
	DSN: 664-7436	Comm: (703) 604-7436
AIM:	Mr. Ray Soroka	ray.soroka@us.army.mil
	DSN: 231-3437	Comm: (540) 731-3437
Training:	Mr. Anthony Lisanti	tony.lisanti@altess.army.mil
View Training Schedule	DSN: 231-3529	Comm: (540) 731-3529

P(S) Application

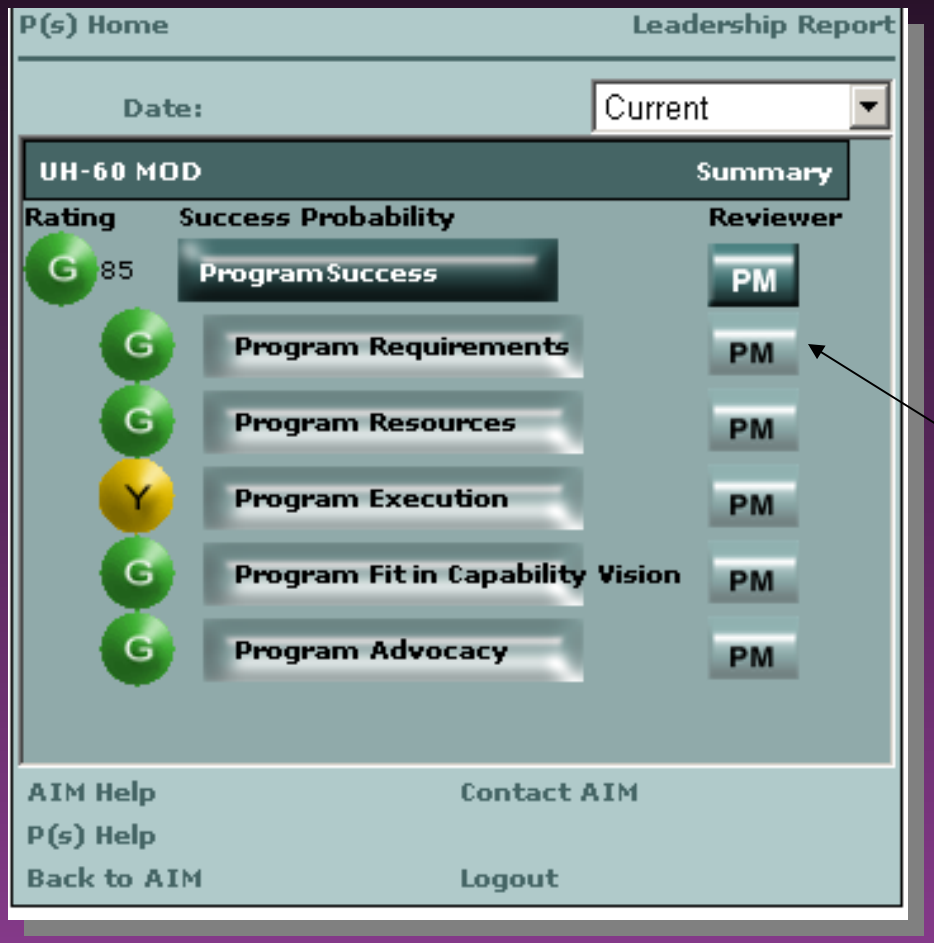

Indicates that this factor is still at the PM level

P(S) Program Requirements

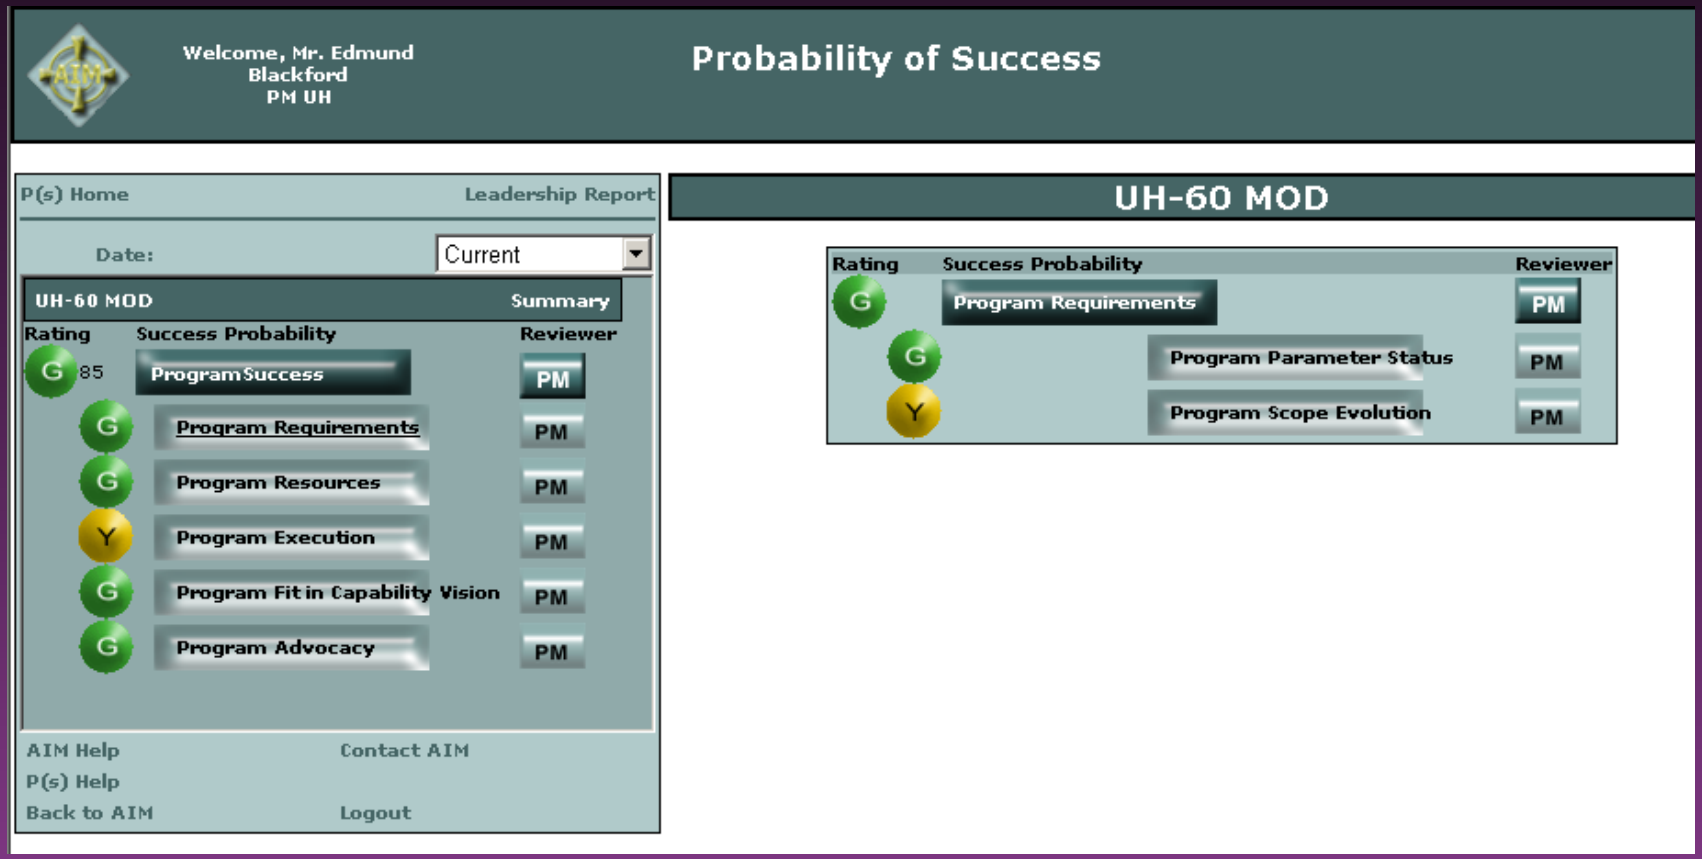

P(S) Program Requirements

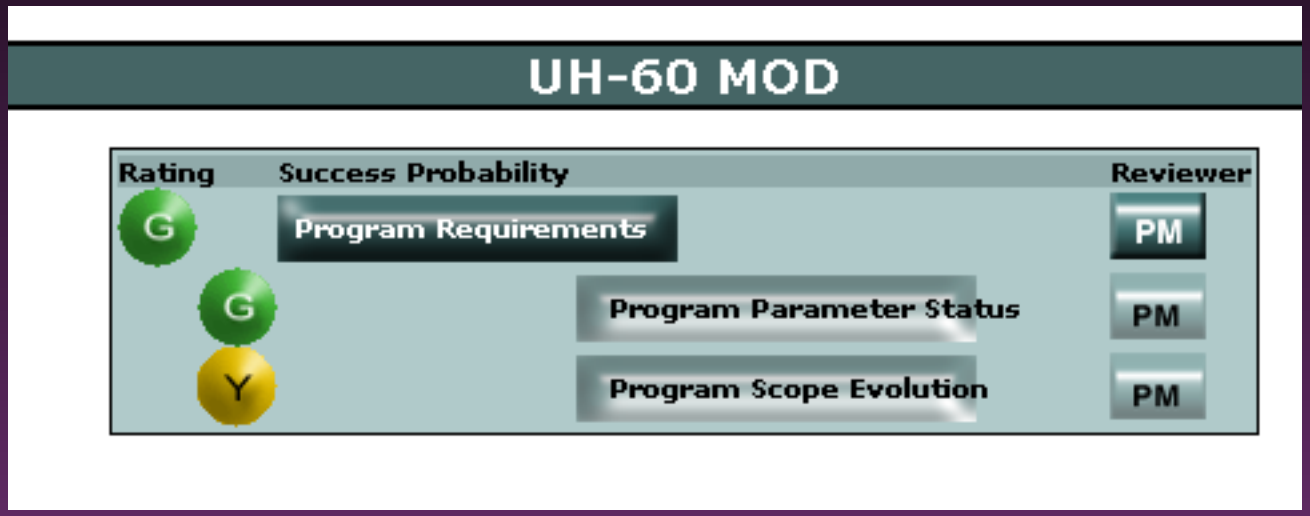

P(S) Program Parameter Status

Welcome, Mr. Edmund Blackford
PM UH

Probability of Success

Program: UH-60 MOD Report Date: Current

Program Parameter Status

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

- To edit the objective, threshold, current value or variance for an existing metric, click the appropriate column for the metric you wish to edit.
- Metrics in the Available Metrics drop-down selection box can be added to the P(s) report by choosing their name.
- Click the "[Add New Metric] link to add a new metric for this program.

Included Metrics

Metric Name	Objective	Threshold	Current Value	Variance
[remove] APUC (BY01$M)	8.565	9.421	9.008	-0.413
[remove] Airspeed (Sus. Cruise) (KTAS)	175	145	146	1
[remove] Combat Radius (KM)	275	225	234	9
[remove] External Lift Payload (lbs)	10000	4500	5336	836
[remove] Interoperability	All	All Critical	All Critical	0
[remove] One Engine Interop (KTAS)	100	100	106	6
[remove] PAUC (BY01$M)	8.851	9.770	9.285	-0.485
[remove] Self-Deploy Range (nm)	1260	1056	1099	43

[Add New Metric]

Available Metrics

Available: - Select Metric To Add - [Add New Metric]

P(S) Scope

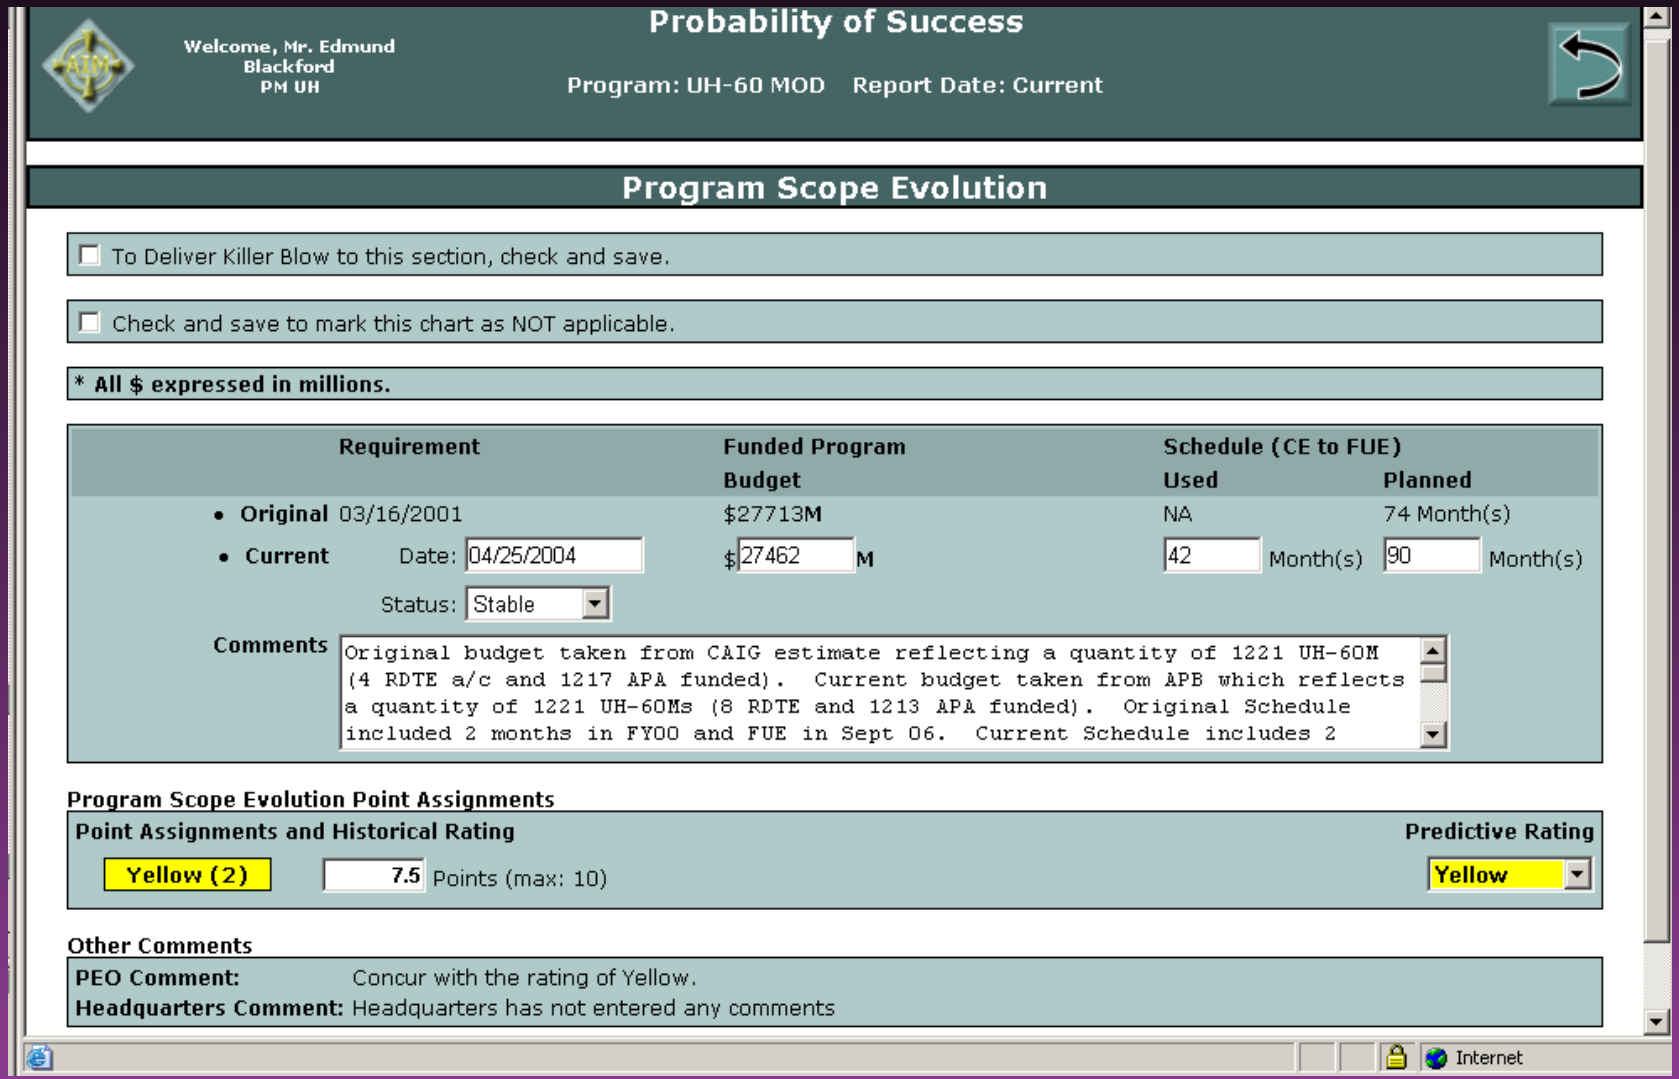

Welcome, Mr. Edmund Blackford
PM UH

Probability of Success

Program: UH-60 MOD Report Date: Current

Program Scope Evolution

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

*** All $ expressed in millions.**

	Requirement	Funded Program Budget	Schedule (CE to FUE) Used	Planned
• **Original**	03/16/2001	$27713M	NA	74 Month(s)
• **Current**	Date: 04/25/2004	$ 27462 M	42 Month(s)	90 Month(s)
	Status: Stable			

Comments

Original budget taken from CAIG estimate reflecting a quantity of 1221 UH-60M (4 RDTE a/c and 1217 APA funded). Current budget taken from APB which reflects a quantity of 1221 UH-60Ms (8 RDTE and 1213 APA funded). Original Schedule included 2 months in FY00 and FUE in Sept 06. Current Schedule includes 2

Program Scope Evolution Point Assignments

Point Assignments and Historical Rating		Predictive Rating
Yellow (2)	7.5 Points (max: 10)	Yellow

Other Comments

PEO Comment: Concur with the rating of Yellow.
Headquarters Comment: Headquarters has not entered any comments

Internet

P(S) Program Resources

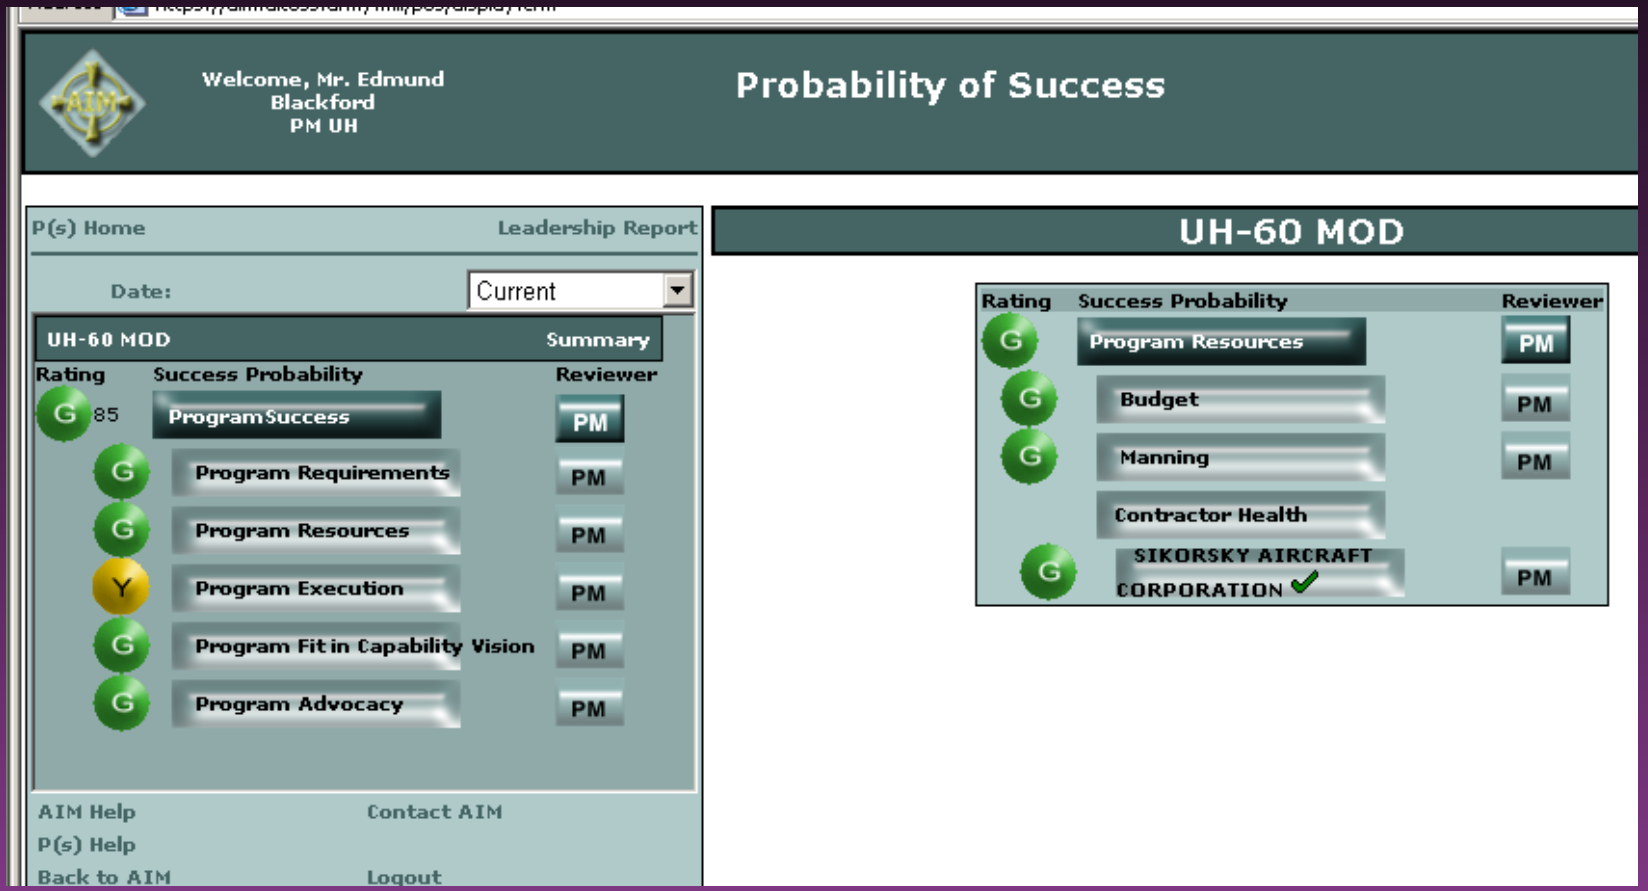

P(S) Budget

Welcome, PM USER
PM TFX

Probability of Success

Program: TFX-01 Report Date: Current

Resources - Budget

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

OSD Goals (Obl/Exp):	First Year	Second Year	Third Year	Army Goals (Obl/Exp):	First Year	Second Year	Third Year

Click on a colored cell in order to cycle the color rating between red, yellow and green.

SUFFICIENT R/Y/G	FY02	OBL/ EXP	FY03	OBL/ EXP	FY04	OBL/ EXP	FY05	FY06	FY07	FY08	FY09	FY10
RDTE	N/A	0% / 0.00%	N/A	0% / 0.00%	N/A	0% / 0.00%	$5771	$5898	$19714	$21409	$10906	$11302
WTCV	N/A	0% / 0.00%	N/A	0% / 0.00%	N/A	0% / 0.00%	$0	$0	$0	$0	$0	$0

[Click to get most recent finacial data] [Click to choose funding lines]

PM Comments (4000 character limit)

FY 01 - 03 is pulled from MAR (DD218)
FY 04-09 is pulled from PROP database
ACFT - APA funding (AA0492) is shared with other BLACK HAWK Modifications, such as Crashworthy External Fuel System, Medical Equipment Package, and other safety modifications.
RDTE - In FY03, FY04, and FY05 respectively, $13.2M, $7M, and $13.1M was added

P(S) Manning

Program Resources - Manning

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

Ending Month

Currently Selected Ending Month: May 2004

Change Ending Month To: May 2004

Included Manning Data

	Civilian		Military		Matrixed		SETA	
	Res.	Vac.	Res.	Vac.	Res.	Vac.	Res.	Vac.
May 2004	2	0	2	1	2	0	0	0
Apr 2004	2	0	8	1	2	0	0	0
Mar 2004	1	5	2	6	2	0	4	8
Feb 2004	10	0	15	1	2	0	2	0
Jan 2004	12	0	15	1	2	0	2	0
Dec 2003	10	2	2	0	2	1	3	0

Full program manning data can be viewed through the Program Manager Application.

PM Comment

No key billets are currently vacant.
The vacancy in Civilian area is a support role and is expected to be filled within the next 3 months.
The Program office is adequately staffed (except as noted above).

Manning Resources Point Assignments

Point Assignments and Historical Rating **Predictive Rating**

P(S) Contractor Health

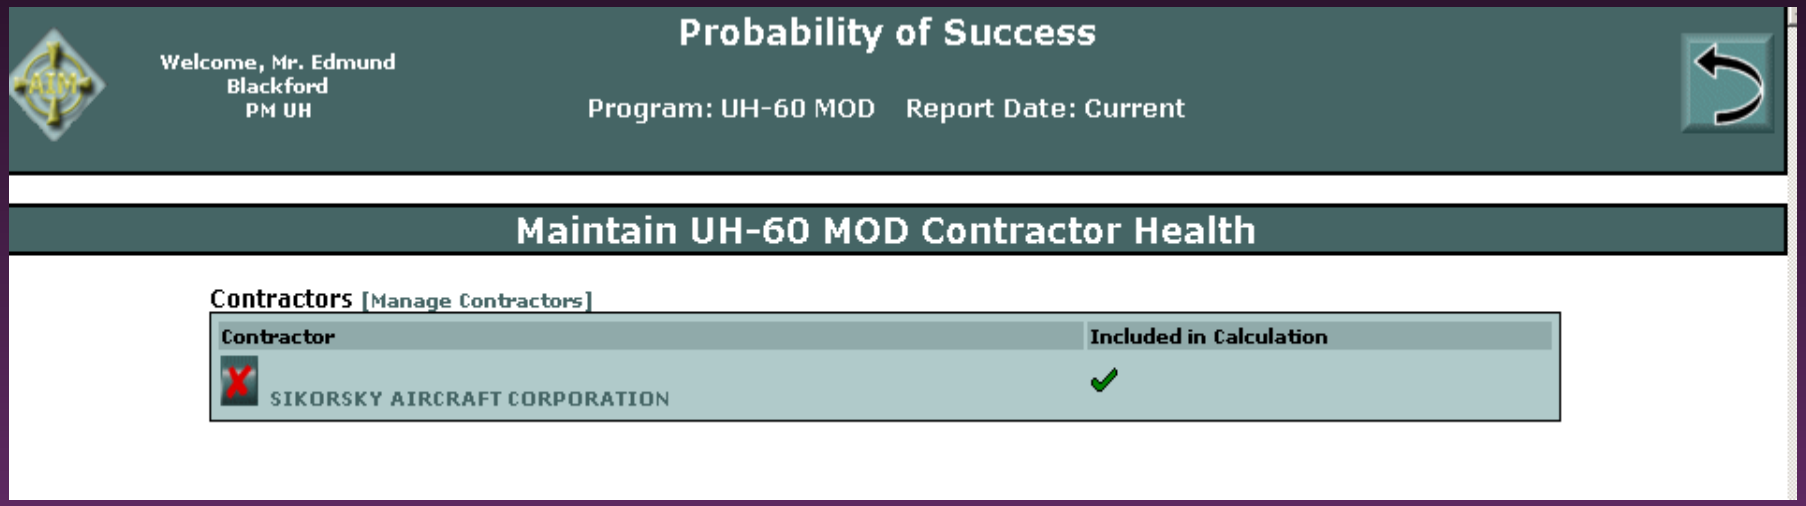

P(S) Contractor Health

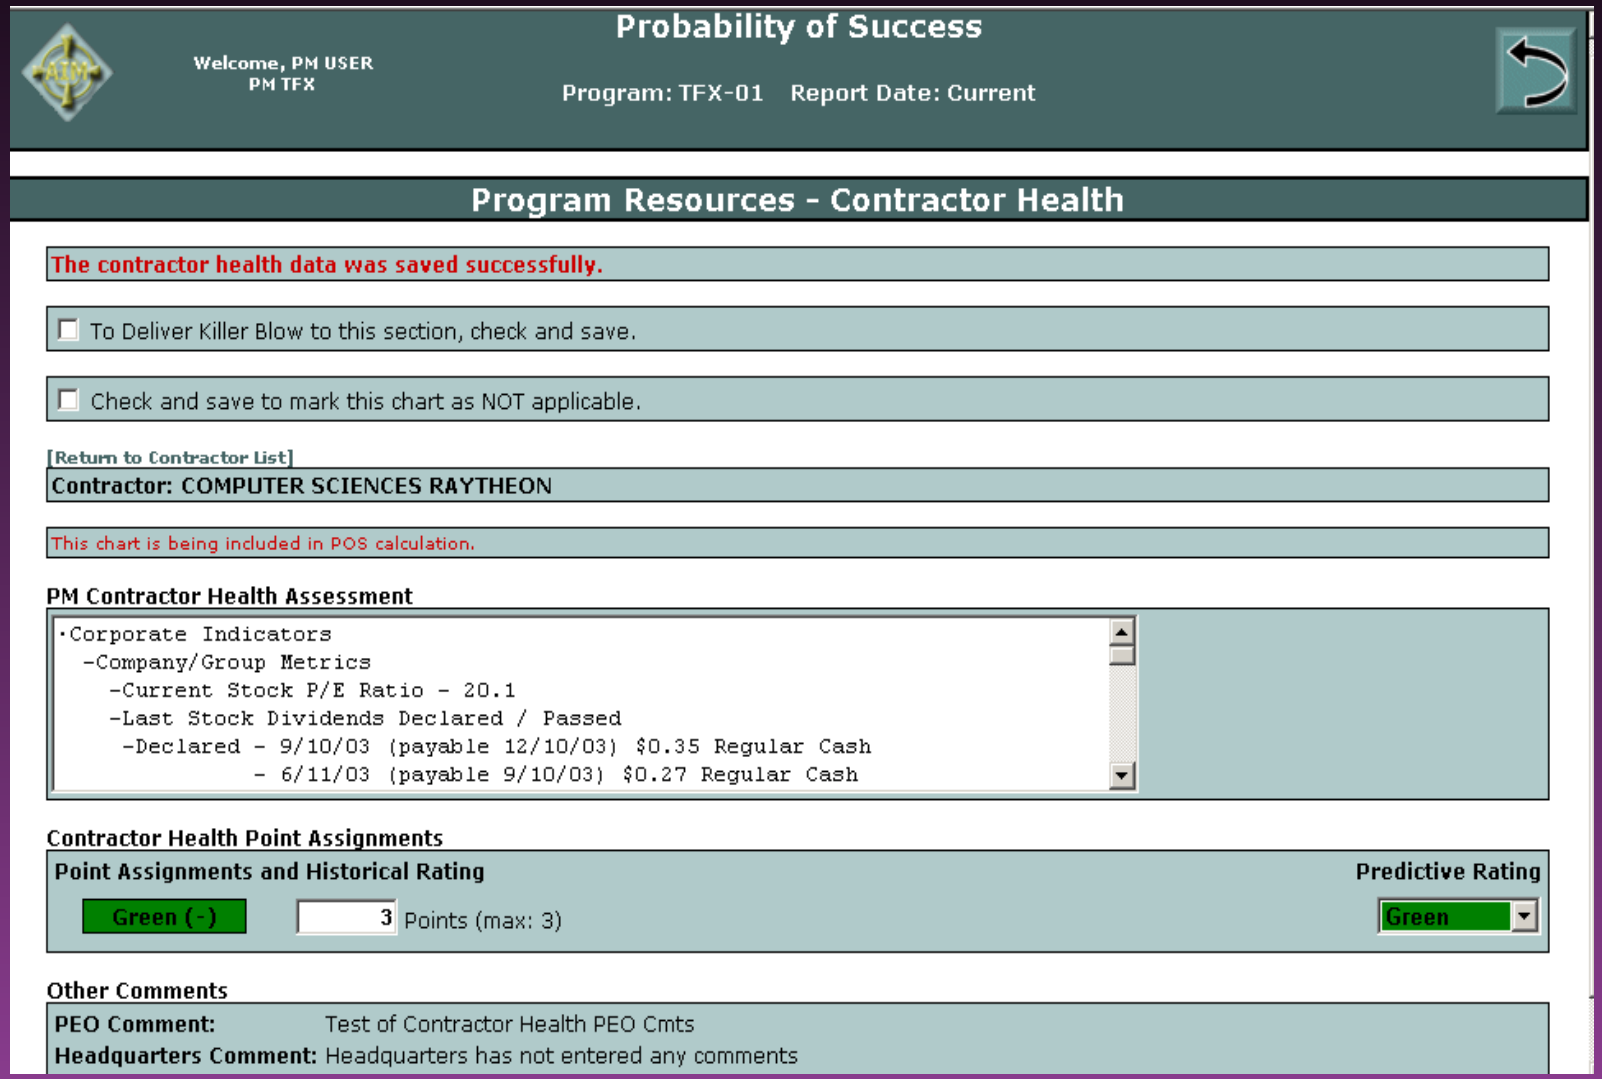

Probability of Success

Welcome, PM USER
PM TFX

Program: TFX-01 Report Date: Current

Program Resources - Contractor Health

The contractor health data was saved successfully.

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

[Return to Contractor List]

Contractor: COMPUTER SCIENCES RAYTHEON

This chart is being included in POS calculation.

PM Contractor Health Assessment

```
·Corporate Indicators
  -Company/Group Metrics
    -Current Stock P/E Ratio - 20.1
    -Last Stock Dividends Declared / Passed
     -Declared - 9/10/03 (payable 12/10/03) $0.35 Regular Cash
               - 6/11/03 (payable 9/10/03) $0.27 Regular Cash
```

Contractor Health Point Assignments

Point Assignments and Historical Rating		Predictive Rating
Green (-)	3 Points (max: 3)	Green

Other Comments

PEO Comment: Test of Contractor Health PEO Cmts

Headquarters Comment: Headquarters has not entered any comments

P(S) Program Execution

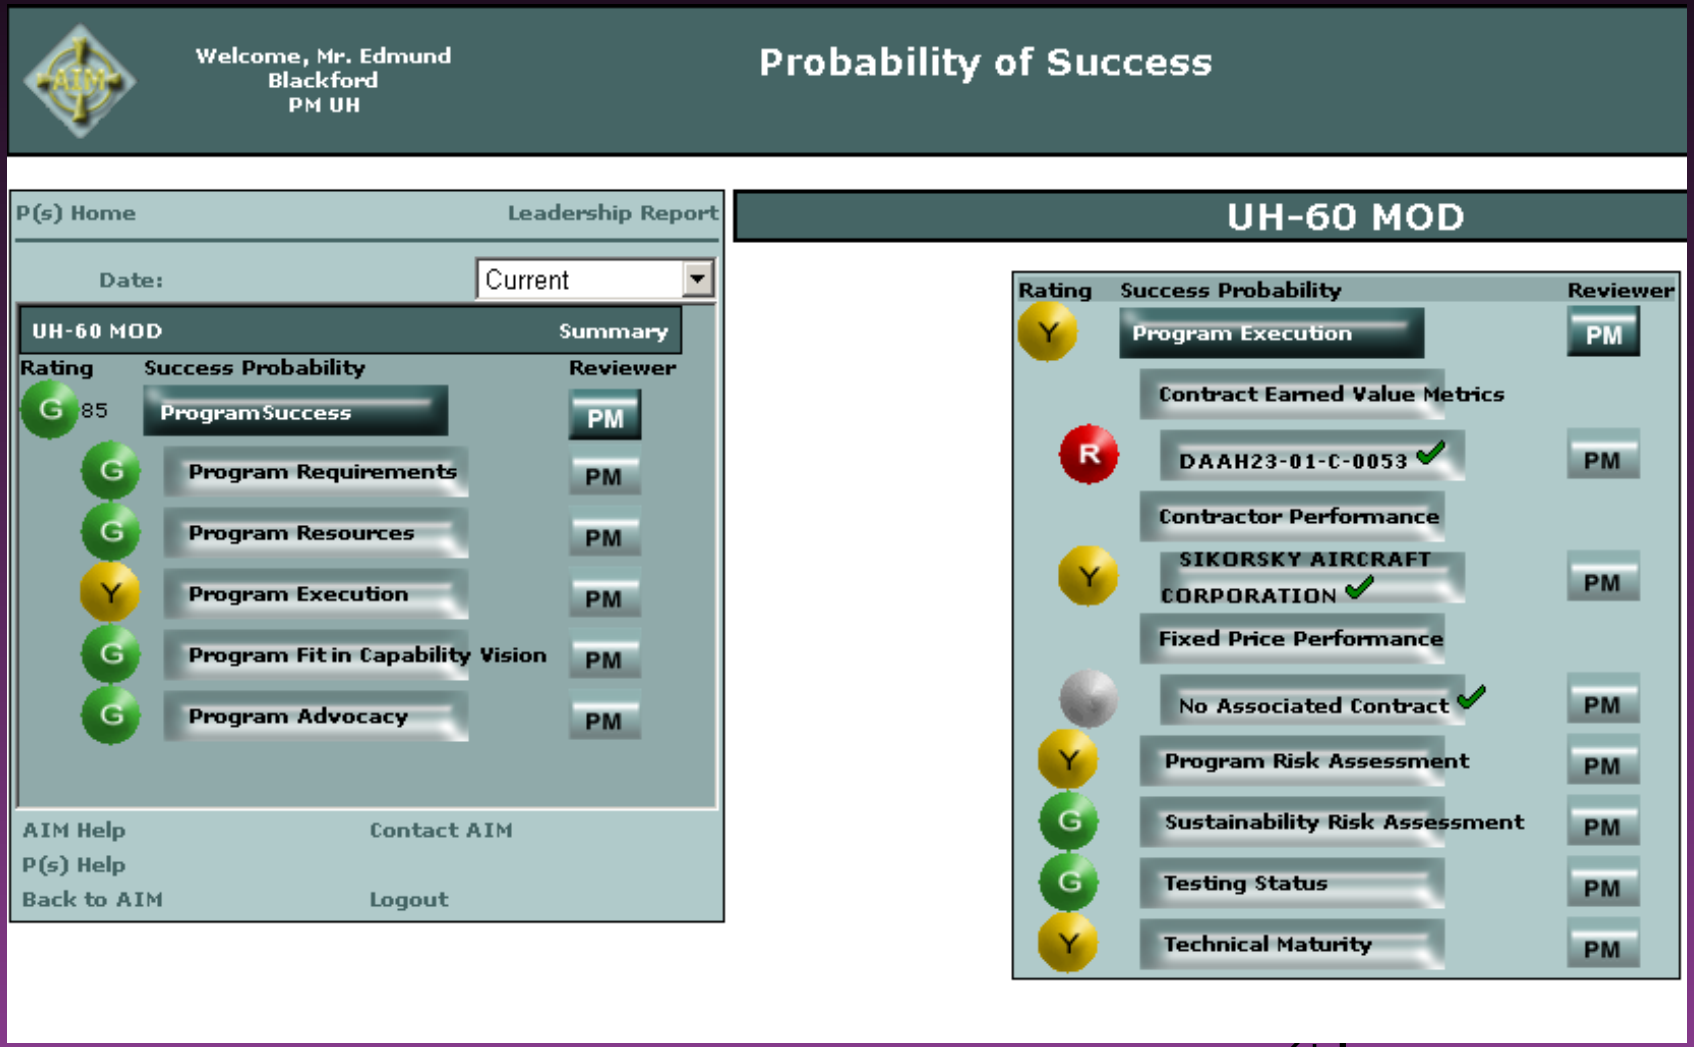

P(S) Earned Value Metrics

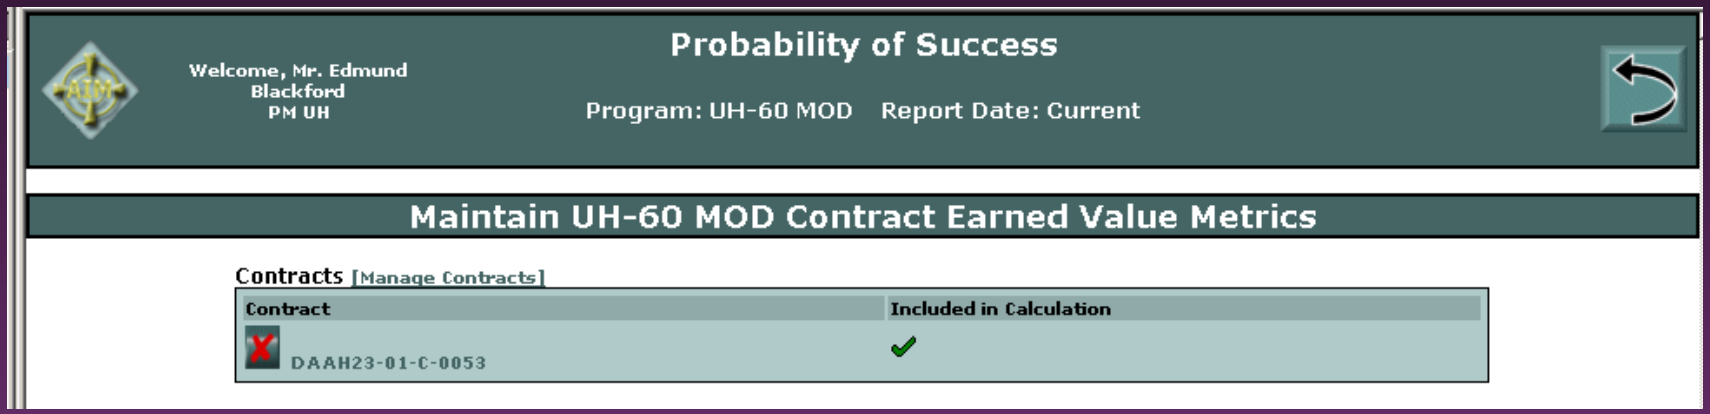

P(S) Earned Value Metrics
Edit Contracts

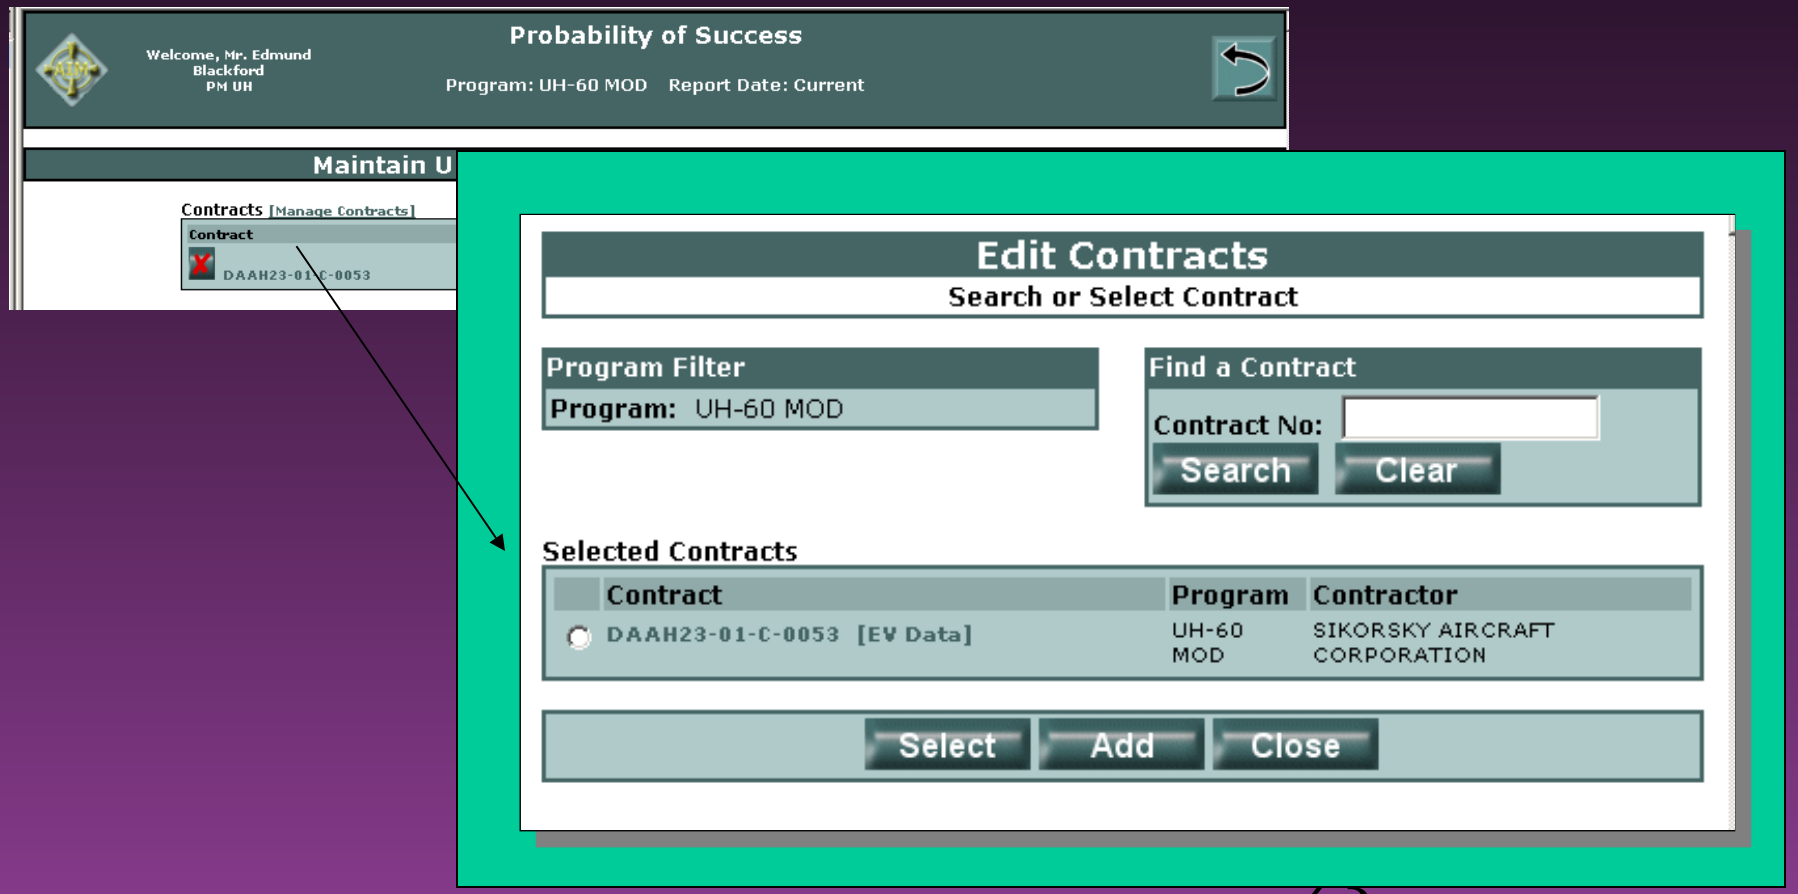

P(S) Earned Value Chart

Current Contract DAAH23-01-C-0053 Earned Value

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

This chart is being included in POS calculation.

CPI and SPI Trend [Manage Contract EV Data] [Included Contracts List]

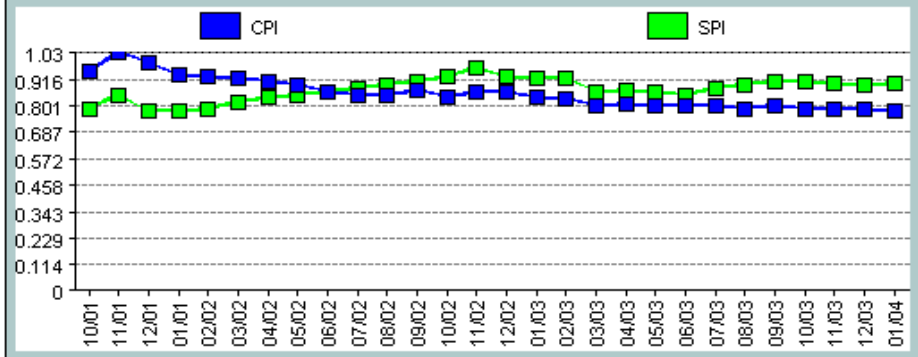



Contract Data

Date of Last Award Fee:		**Last Program Rebaselining Date:**	
Date of Next Award Fee:		**Number of Program Rebaselinings:**	
CV:	-39.18	**SV:**	-13.11
TCPI:	0.88		

P(S) Earned Value Chart

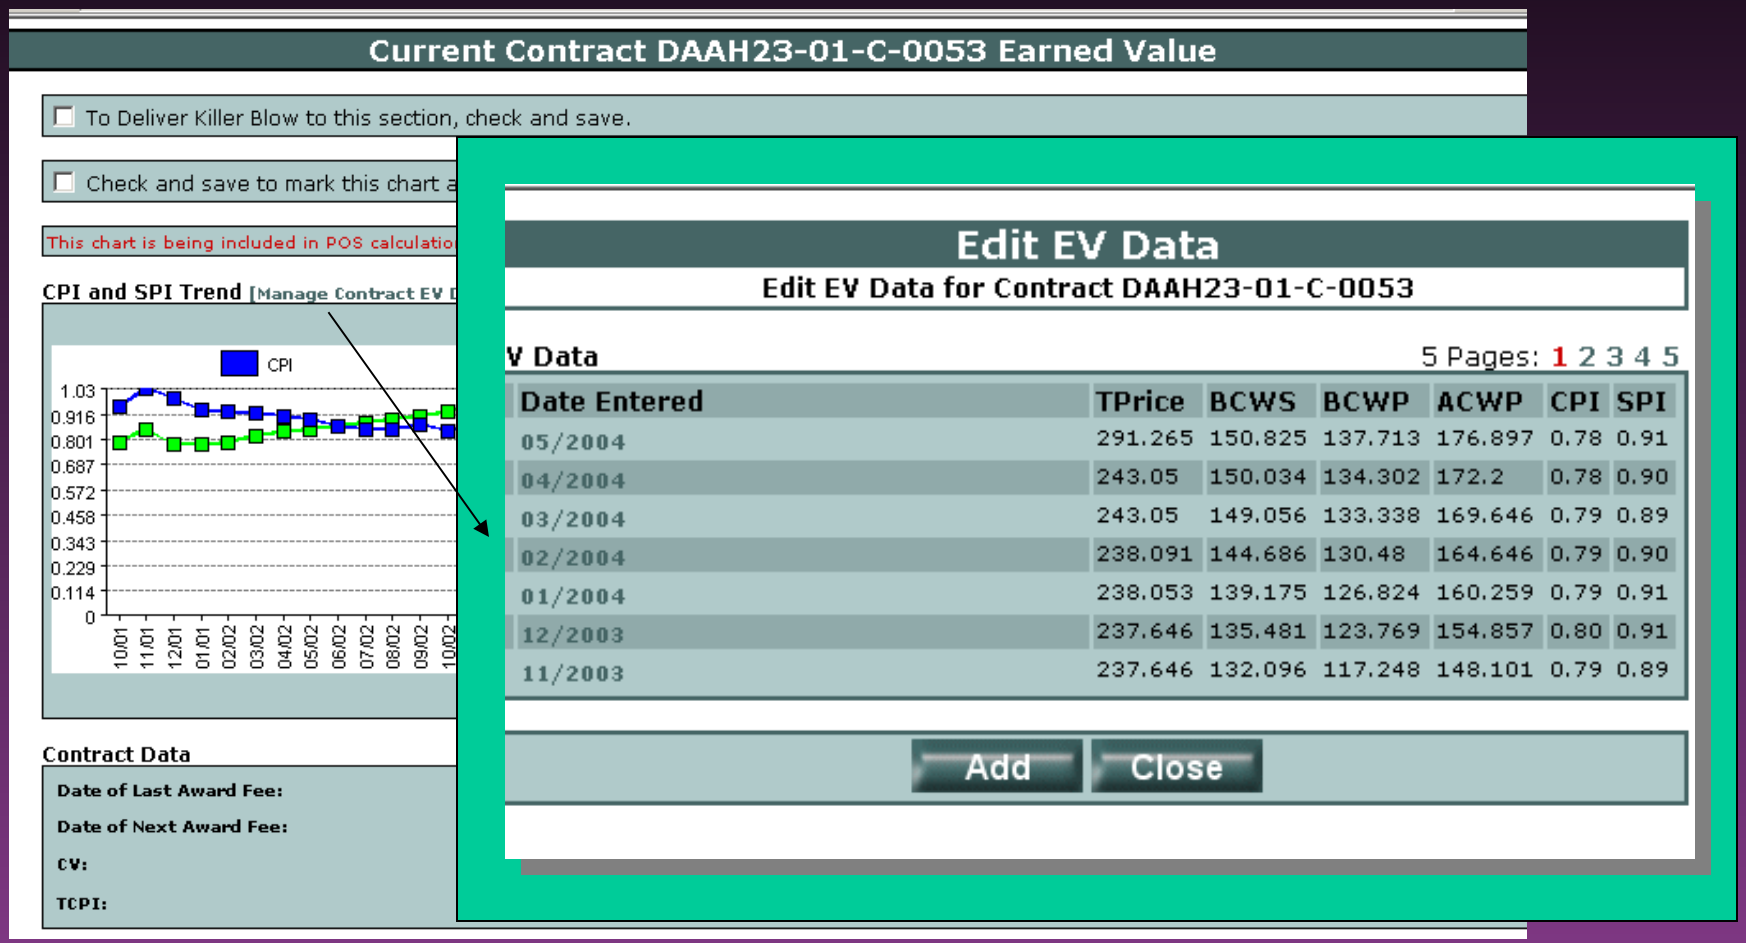

P(S) Earned Value Chart

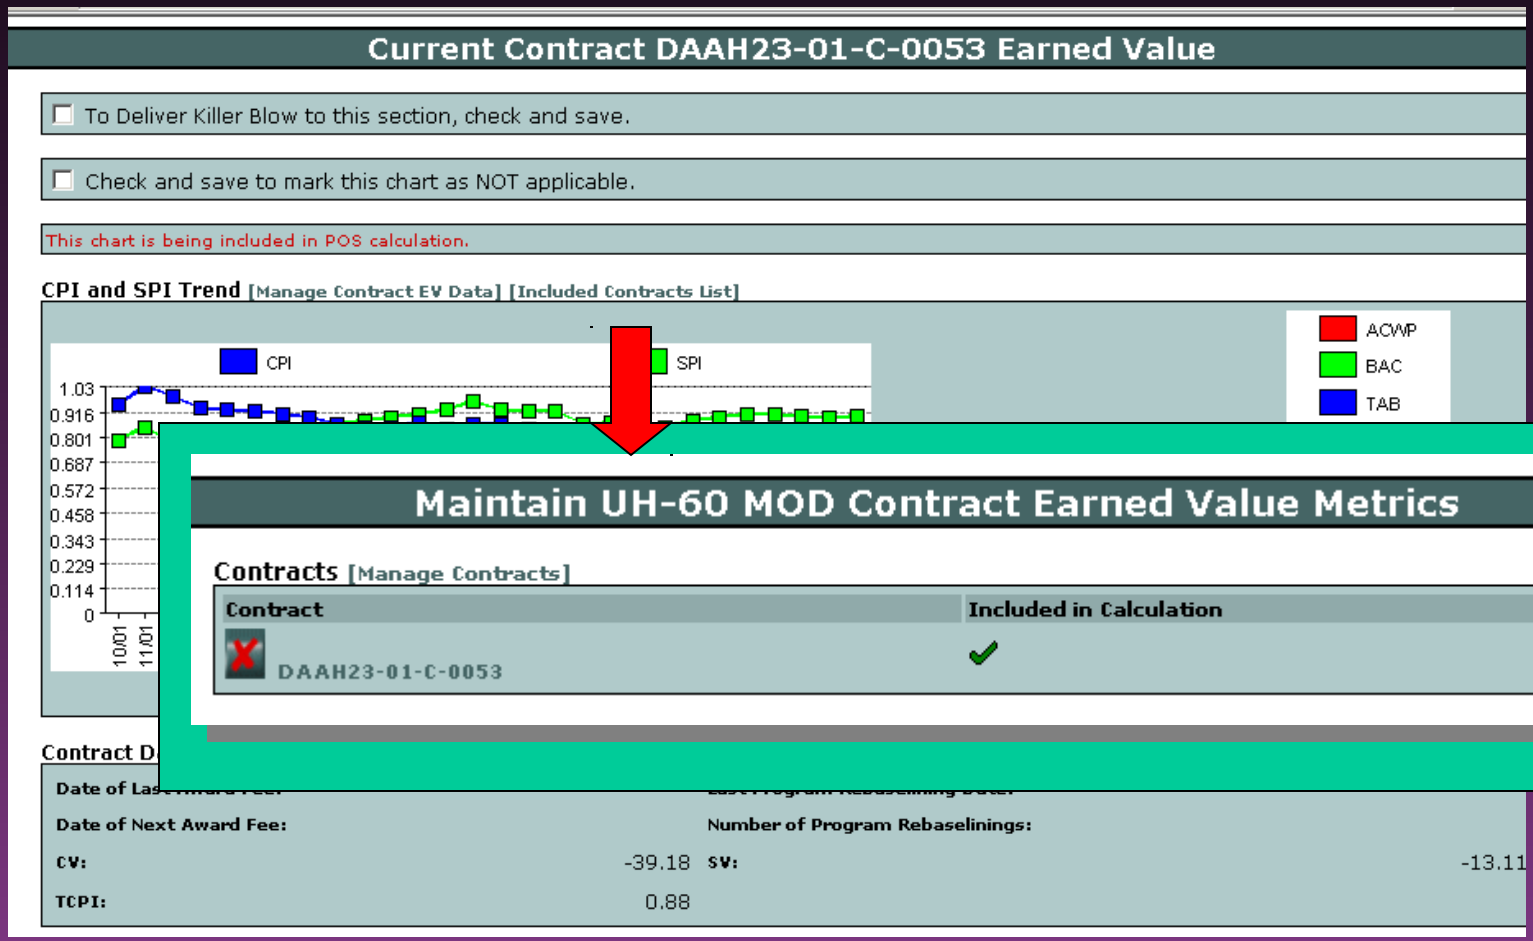

P(S)Contactor Performance

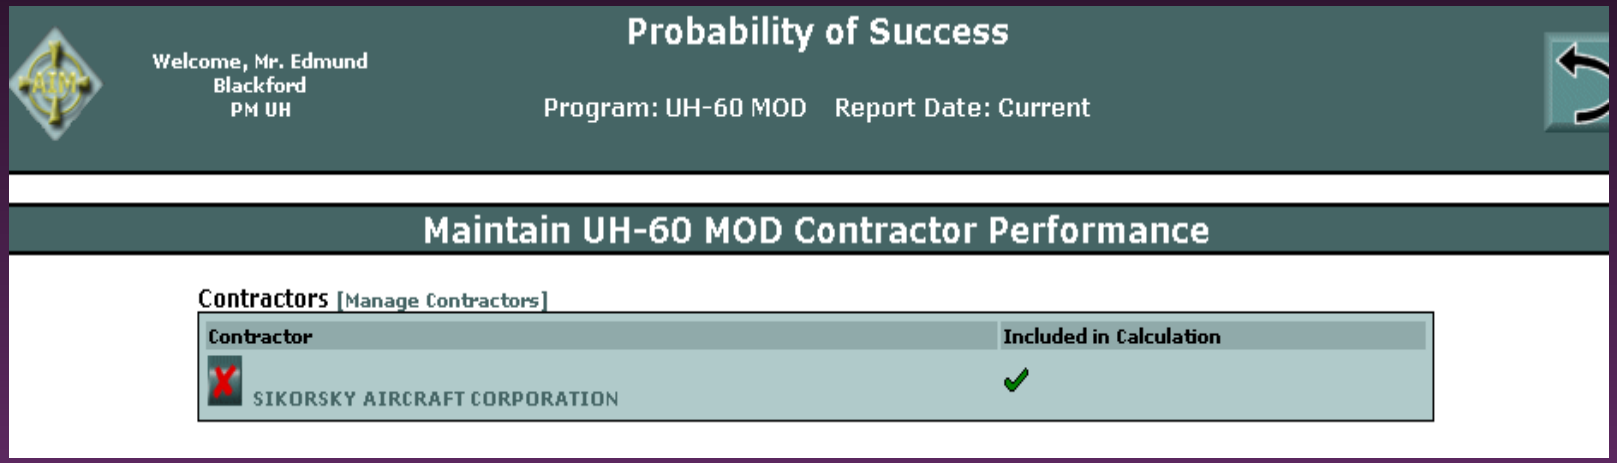

P(S)Contactor Performance

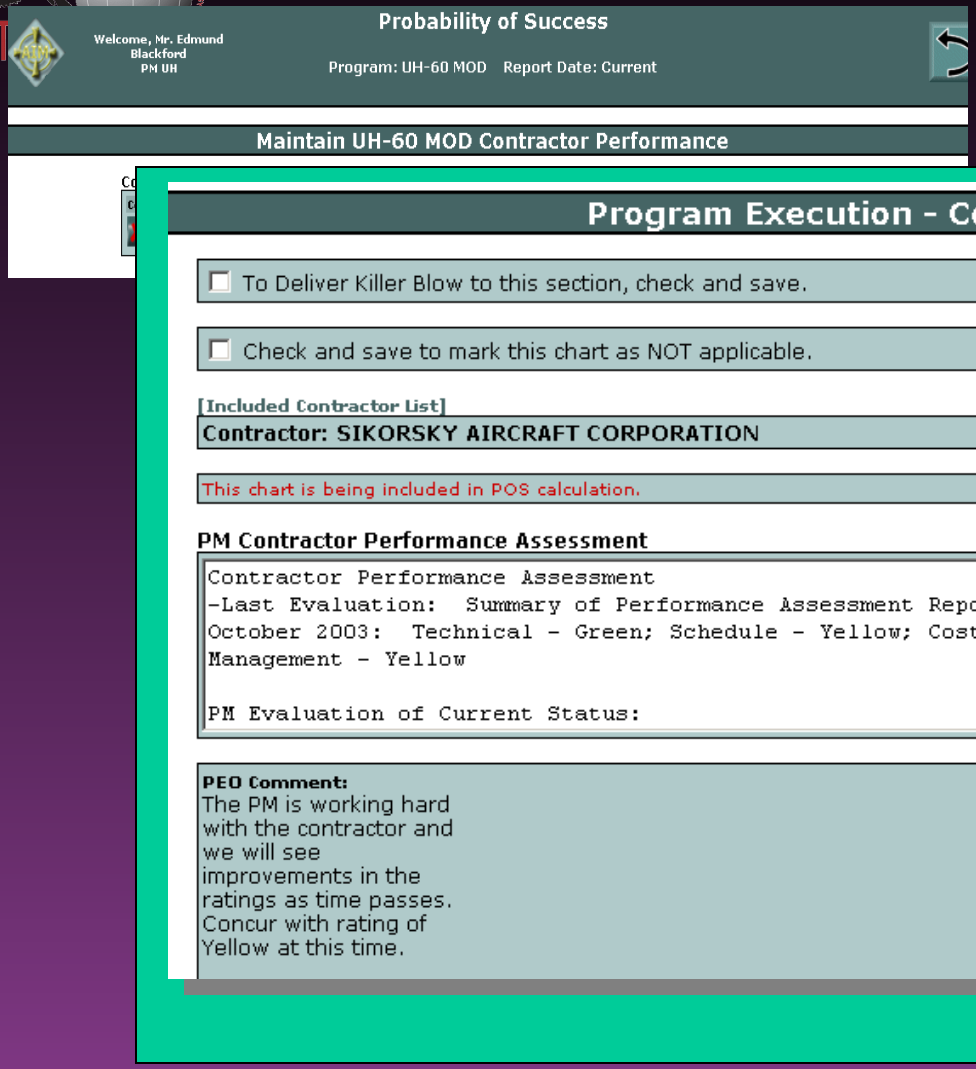
Welcome, Mr. Edmund Blackford
PM UH
Probability of Success
Program: UH-60 MOD Report Date: Current
Maintain UH-60 MOD Contractor Performance
Program Execution - Contractor Performance
To Deliver Killer Blow to this section, check and save.
Check and save to mark this chart as NOT applicable.
[Included Contractor List]
Contractor: SIKORSKY AIRCRAFT CORPORATION
This chart is being included in POS calculation.
PM Contractor Performance Assessment
Contractor Performance Assessment
-Last Evaluation: Summary of Performance Assessment Report Quarter ending October 2003: Technical - Green; Schedule - Yellow; Cost Control - Yellow; Management - Yellow
PM Evaluation of Current Status:
PEO Comment:
The PM is working hard with the contractor and we will see improvements in the ratings as time passes. Concur with rating of Yellow at this time.

P(S) Risk Management

Current Program Risk Assessments

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.



Selected Risks [Maintain Risks]

Risk	Description	Likelihd.	Conseq.	Rating/Trend	Mitigation Plan
Flight Management System (FMS) Build C (MEP)	Dual Flight Management System (FMS) SW problems with Build A/B carried forward to Build C. Currently 4 months behind schedule. SAC experiencing staffing problems. FMS Build C software is required for Limited User Test (LUT) and avionics flight tests. LUT would be delayed which may delay MS C.	2	4	Y (-)	[Edit] LUT in the SIL functionality has been prioritized for build C to meet requirements.
LUT in the SIL Execution	HW and SW components (MFDs, FMSs, E-Ports, etc) need to be delivered in a timely manner. LUT in the SIL is the key event to going to MS C; big increase to cost and schedule impact if not met.	1	4	G (-)	[Edit] Added technician to recover 3 weeks of HW assembly schedule. Conduct weekly LUT in the SIL progress reviews. Micro-managing HW and SW deliveries and issues on a daily basis.
Earned Value Management	EVMS controls have not been followed (Level III Corrective Action Report issued by DCMA). Lack of EVMS compliance contributed to current program restructure (APB RDT&E Cost Breach). SAC has shown improvements in EV processes, however, continued management emphasis is required to	2	5	Y (-)	[Edit] Increased DCMA oversight. Increased PM oversight and communications. Conduct 2 additional Integrated Baseline Reviews. Accurate and timely CPRs/CFSRs.

P(S) Current Sustainability Risk Assessment

Current Sustainability Risk Assessment

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.



Sustainment Risks

Risk	Description	Likelihd.	Conseq.	Rating/Trend	Mitigation Plan
Training	[Edit] The current training approach is based on a three level maintenance concept. There will be an impact to AVIM level training when a two level maintenance concept is implemented. There is cost risk due to changing training package requirements (IMI, POI, etc).	4	1	G (-)	[Edit] Get user concurrence to develop training under two level maintenance and mod contract to change maintenance concept.
Supply Support	[Edit] Current Supply Support is based on a three level maintenance concept, changing to two level at end of development cycle may have cost impacts due to increased logistics pipeline requirements as well as ASL/PLL increases.	4	1	G (-)	[Edit] Get user concurrence to provision under two level maintenance and mod contract to change maintenance concept.
Publications	[Edit] Current manuals are being developed under three level maintenance concept. Change to two level maintenance concept will impact all -23 manuals. There will be cost impact to change all manuals.	5	1	Y (-)	[Edit] Get user concurrence to develop manuals under two level maintenance and mod contract to change maintenance concept.
Maintenance Concept	[Edit] Based on current ORD requirements, the HH/UH-60M build is under three level maintenance concept. Changing to a two level maintenance concept (Field and	5	1	Y (-)	[Edit] Get user concurrence to change ORD three level requirements to two level maintenance and mod contract to change maintenance concept.

P(S) Technical Maturity

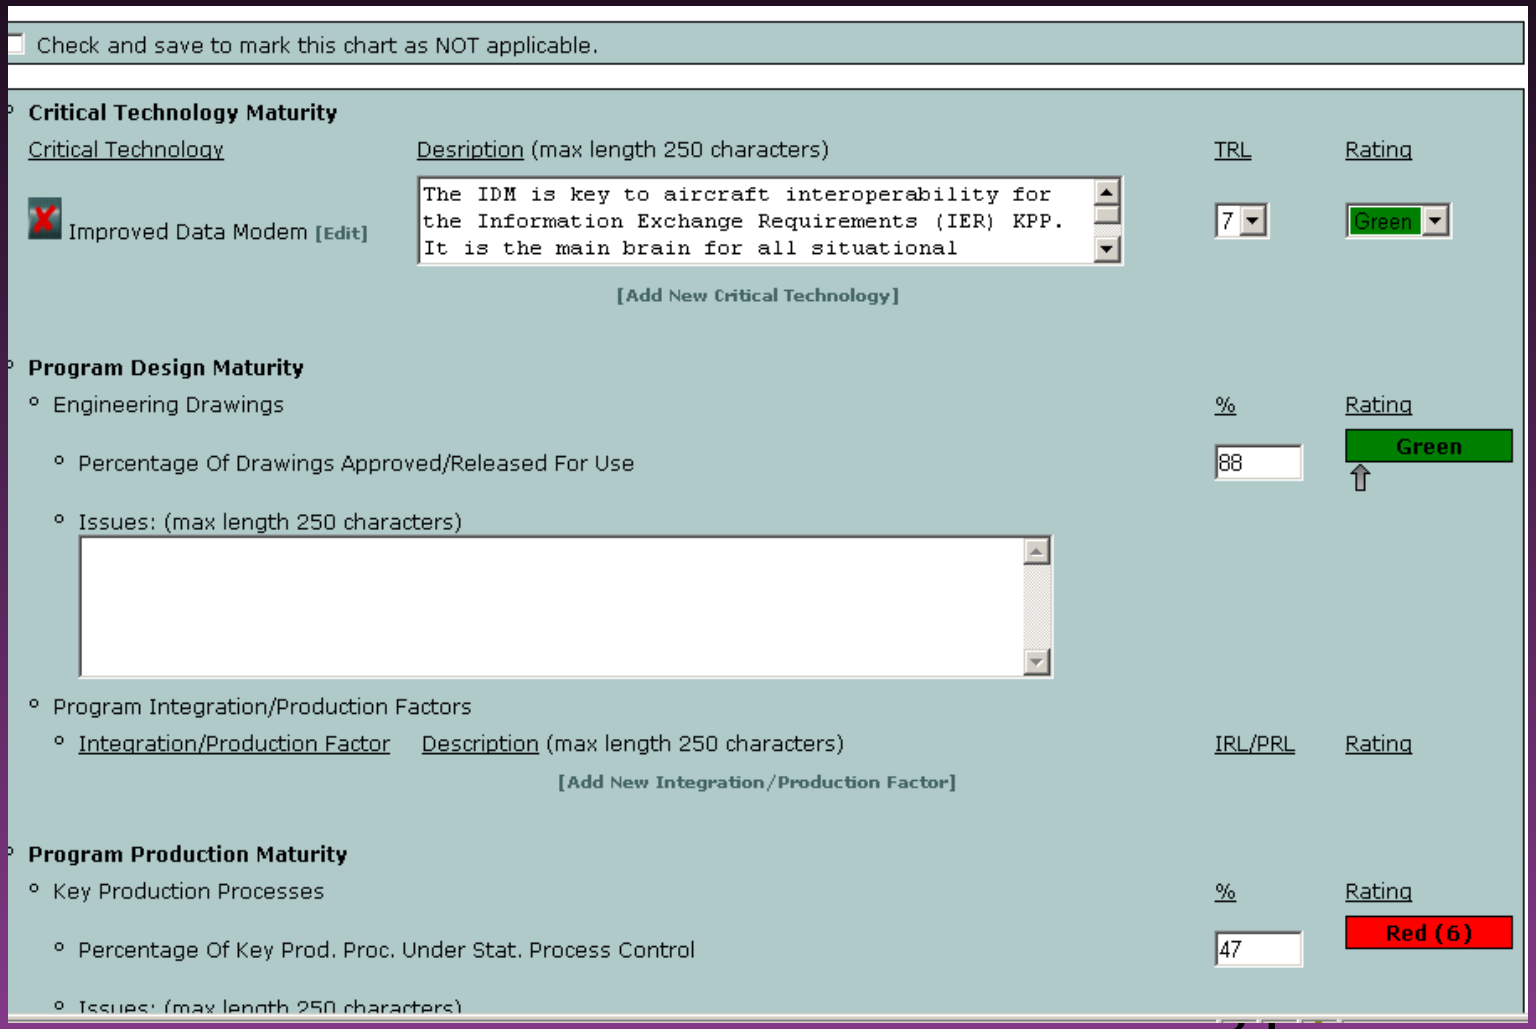

P(S)Testing Status

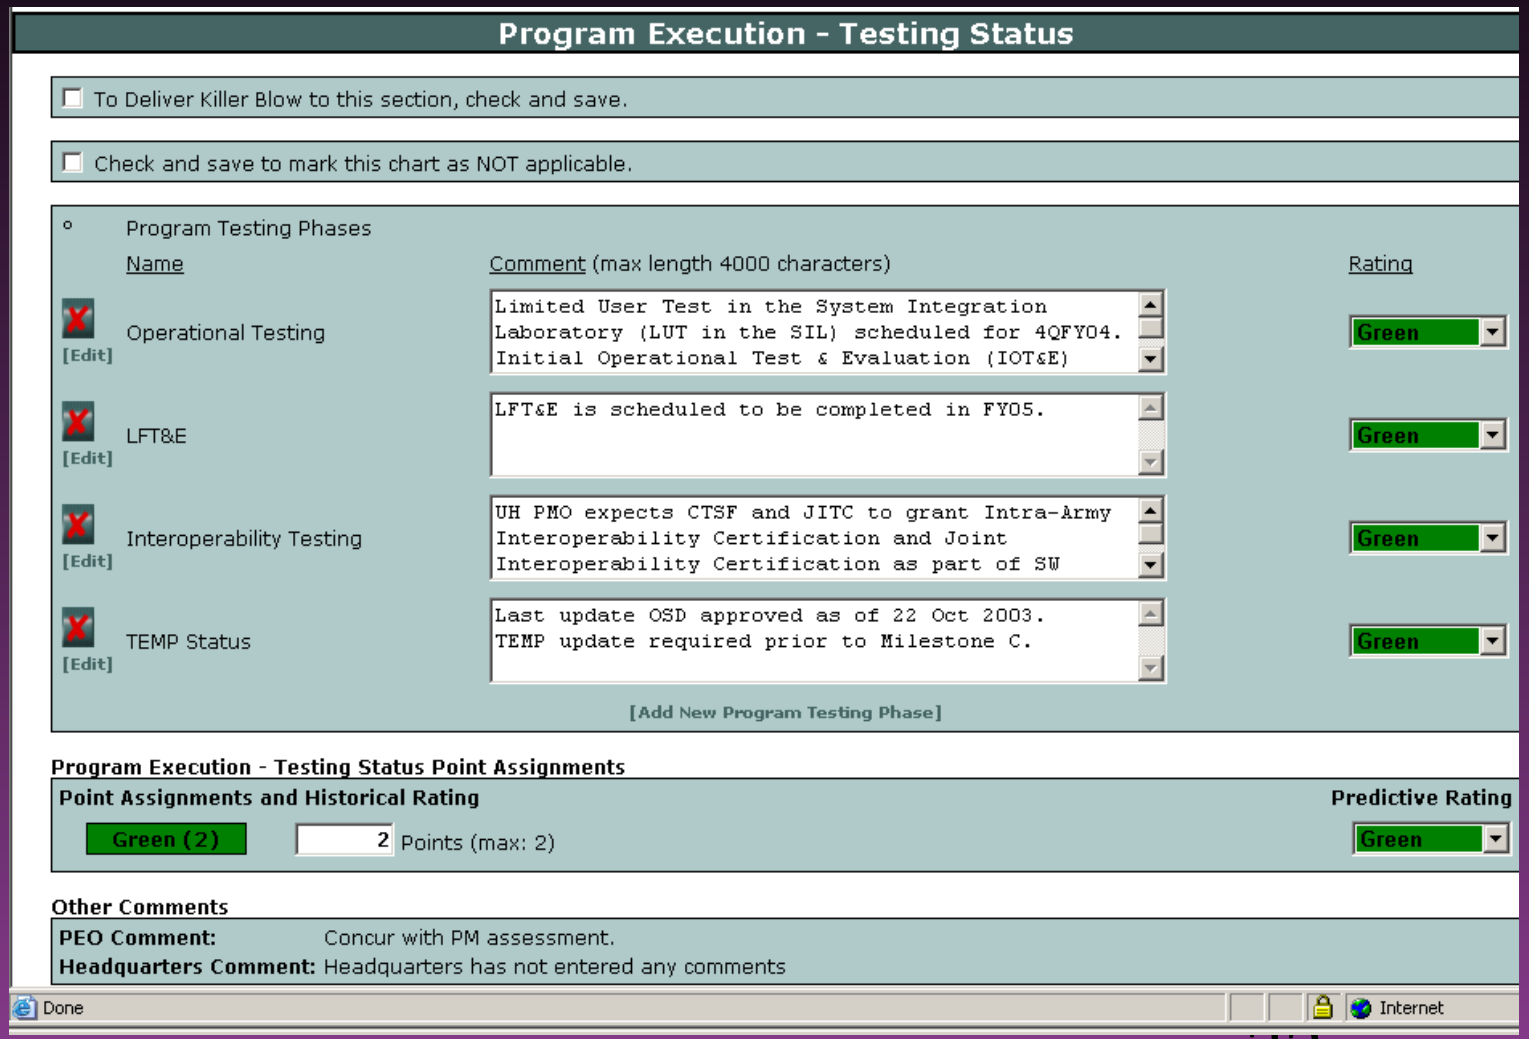

Program Execution - Testing Status

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

° Program Testing Phases

Name	Comment (max length 4000 characters)	Rating
[Edit] Operational Testing	Limited User Test in the System Integration Laboratory (LUT in the SIL) scheduled for 4QFY04. Initial Operational Test & Evaluation (IOT&E)	Green
[Edit] LFT&E	LFT&E is scheduled to be completed in FY05.	Green
[Edit] Interoperability Testing	UH PMO expects CTSF and JITC to grant Intra-Army Interoperability Certification and Joint Interoperability Certification as part of SW	Green
[Edit] TEMP Status	Last update OSD approved as of 22 Oct 2003. TEMP update required prior to Milestone C.	Green

[Add New Program Testing Phase]

Program Execution - Testing Status Point Assignments

Point Assignments and Historical Rating | **Predictive Rating**

Green (2) | 2 Points (max: 2) | Green

Other Comments

PEO Comment: Concur with PM assessment.

Headquarters Comment: Headquarters has not entered any comments

Done | Internet

P(S) Program Fit

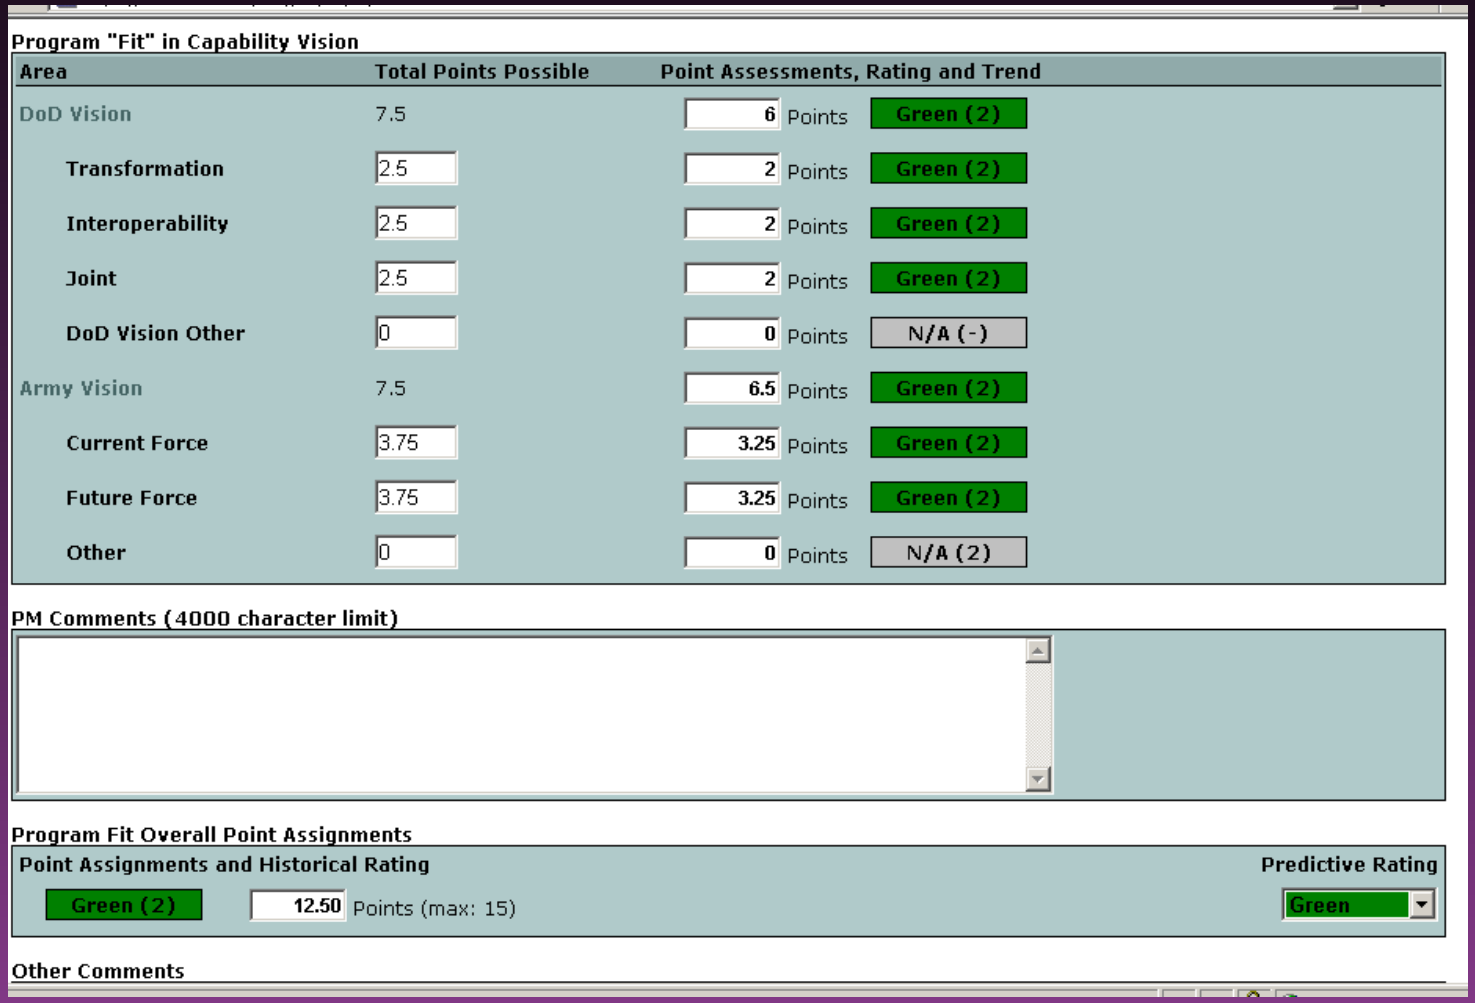

Program "Fit" in Capability Vision

Area	Total Points Possible	Point Assessments, Rating and Trend
DoD Vision	7.5	6 Points — Green (2)
Transformation	2.5	2 Points — Green (2)
Interoperability	2.5	2 Points — Green (2)
Joint	2.5	2 Points — Green (2)
DoD Vision Other	0	0 Points — N/A (-)
Army Vision	7.5	6.5 Points — Green (2)
Current Force	3.75	3.25 Points — Green (2)
Future Force	3.75	3.25 Points — Green (2)
Other	0	0 Points — N/A (2)

PM Comments (4000 character limit)

Program Fit Overall Point Assignments

Point Assignments and Historical Rating		Predictive Rating
Green (2)	12.50 Points (max: 15)	Green

Other Comments

P(S) Program Advocacy

Program Advocacy

☐ To Deliver Killer Blow to this section, check and save.

☐ Check and save to mark this chart as NOT applicable.

Program Advocacy Areas

Area	Total Points Possible	Assessed Points, Rating and Trend
✖ OSD	5	5 Points — Green (2)
	PEO Comment:	
✖ Joint Staff	4	4 Points — Green (2)
	PEO Comment:	
✖ War Fighter	4	4 Points — Green (2)
	PEO Comment:	
✖ Army Secretariat	5	5 Points — Green (2)
	PEO Comment:	
✖ Congressional	5	5 Points — Green (2)
	PEO Comment:	
✖ Industrial	2	1.7 Points — Green (2)
	PEO Comment:	
✖ International	0	0 Points — N/A (2)
	PEO Comment:	

Other Available Areas: There are no other areas available to be added [Request New Area]

Program Advocacy Overall Point Assignments

Point Assignments and Historical Rating	Predictive Rating

P(S) Program Success

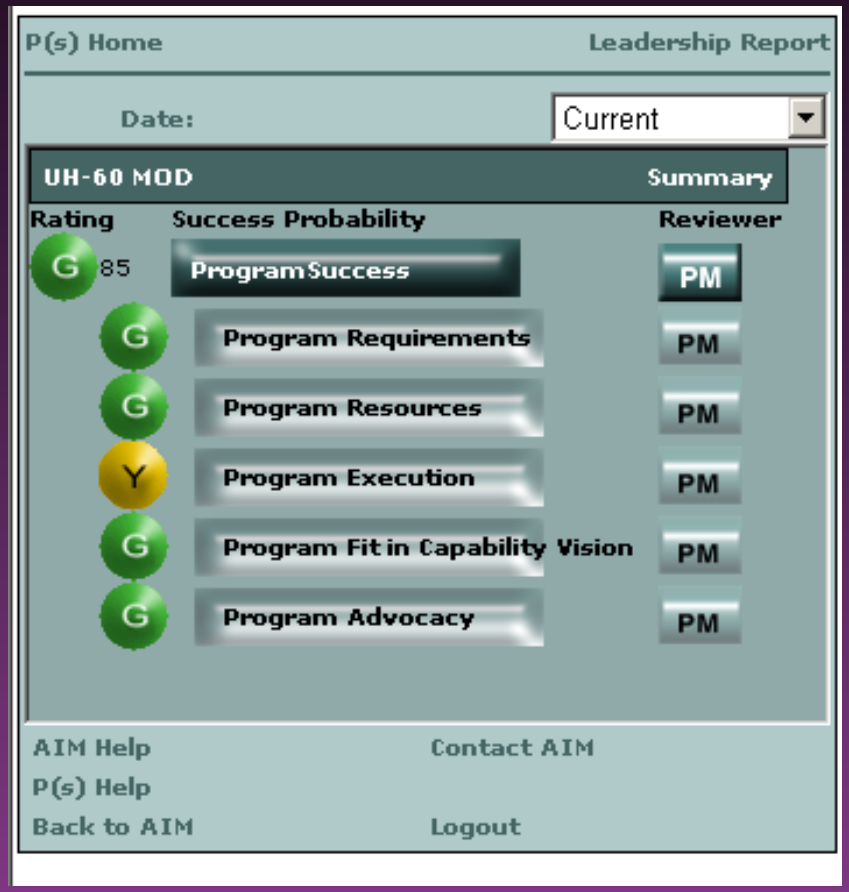

P(S) Closer

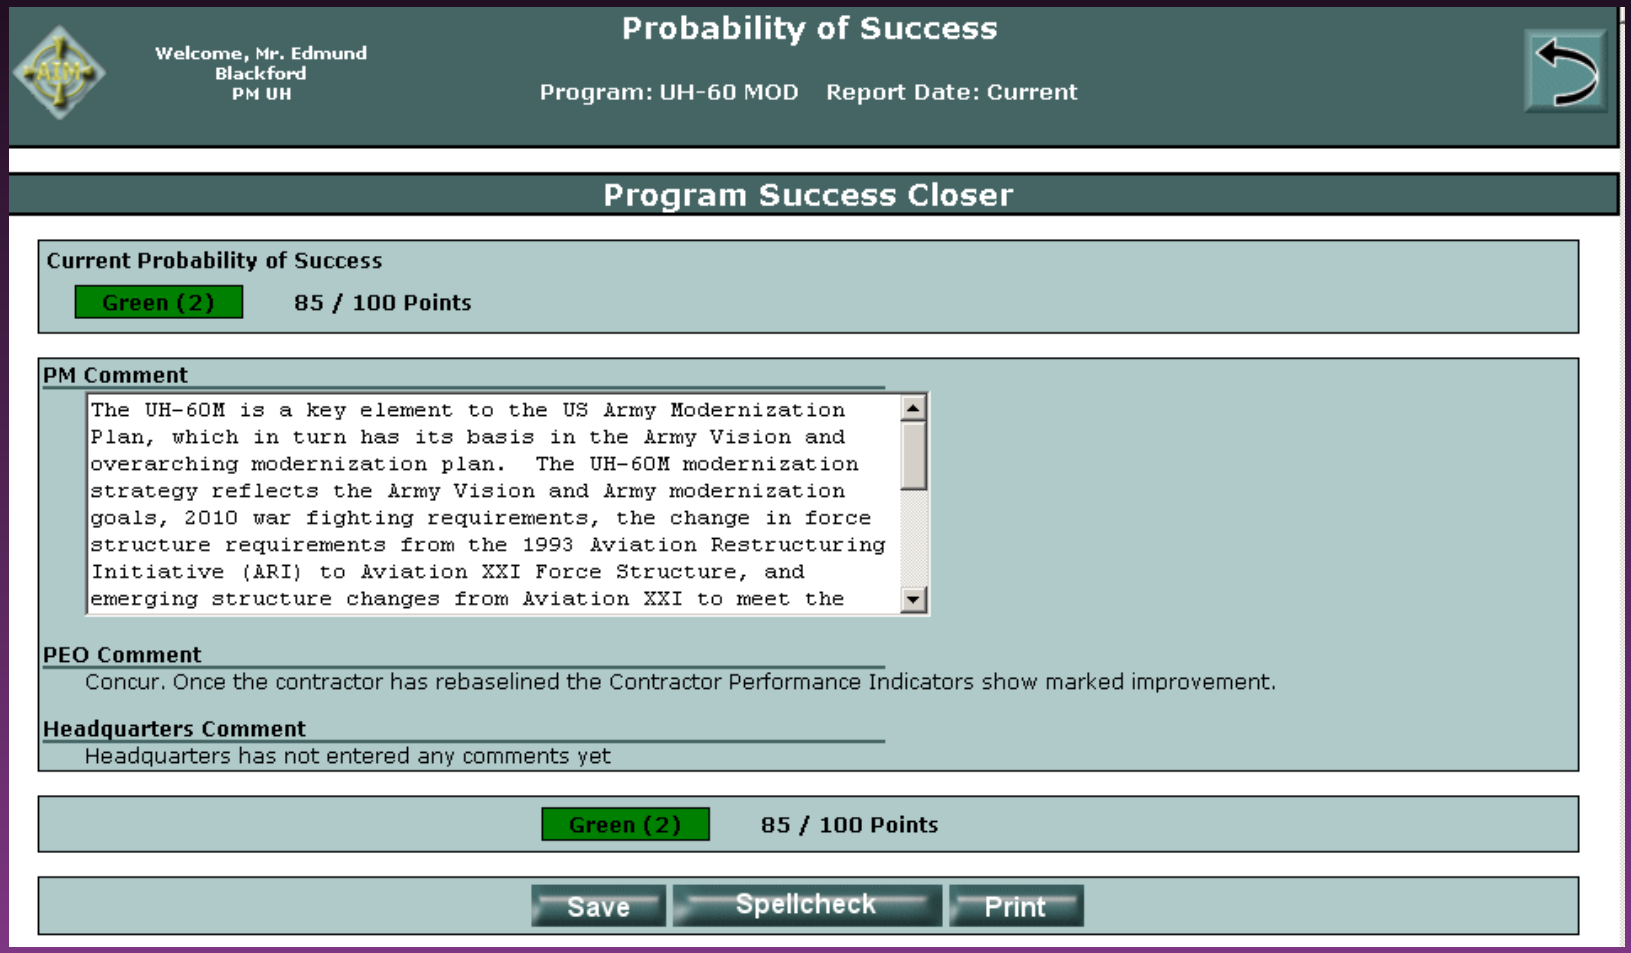
Welcome, Mr. Edmund Blackford
PM UH
Probability of Success
Program: UH-60 MOD Report Date: Current
Program Success Closer
Current Probability of Success
Green (2)
85 / 100 Points
PM Comment
The UH-60M is a key element to the US Army Modernization Plan, which in turn has its basis in the Army Vision and overarching modernization plan. The UH-60M modernization strategy reflects the Army Vision and Army modernization goals, 2010 war fighting requirements, the change in force structure requirements from the 1993 Aviation Restructuring Initiative (ARI) to Aviation XXI Force Structure, and emerging structure changes from Aviation XXI to meet the
PEO Comment
Concur. Once the contractor has rebaselined the Contractor Performance Indicators show marked improvement.
Headquarters Comment
Headquarters has not entered any comments yet
Green (2)
85 / 100 Points
Save
Spellcheck
Print

P(S) Leadership Report

Click to access leadership report summary

P(S) Leadership Report

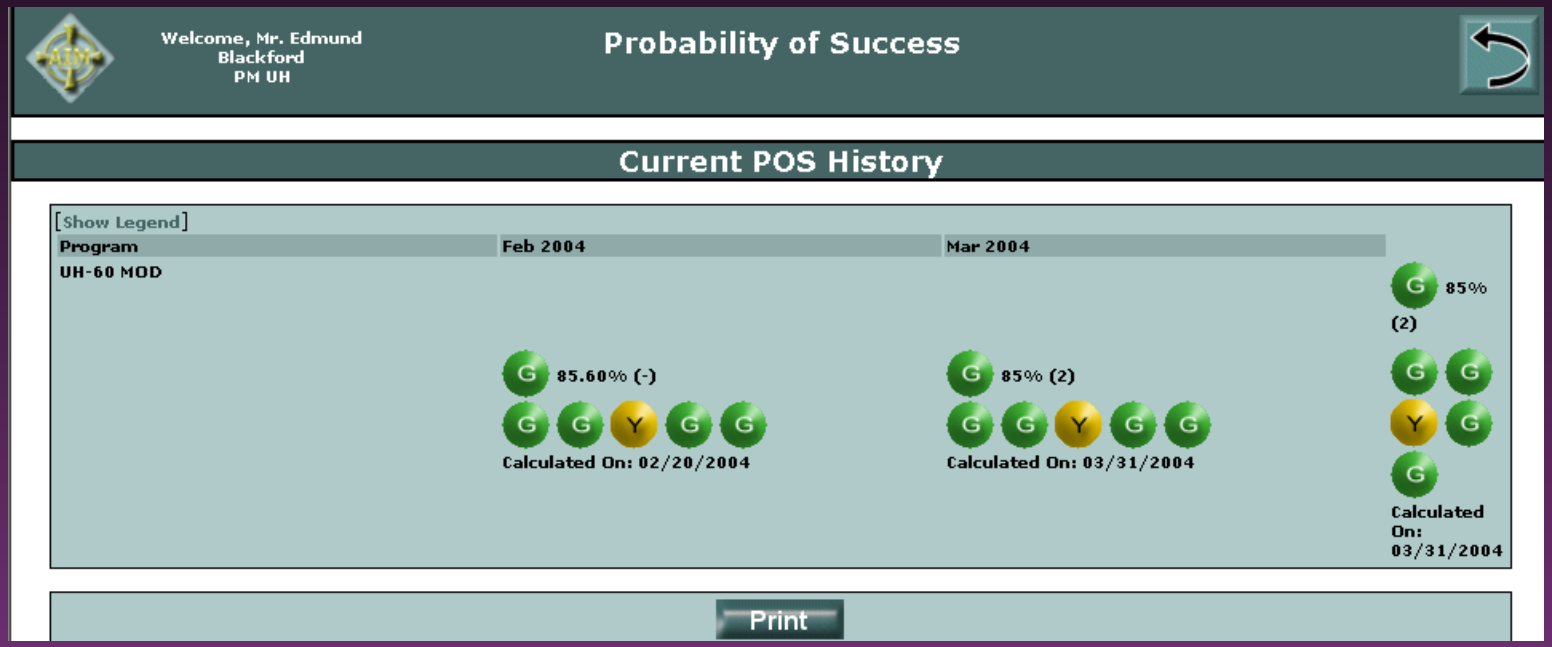

P(S) Leadership Report Legend

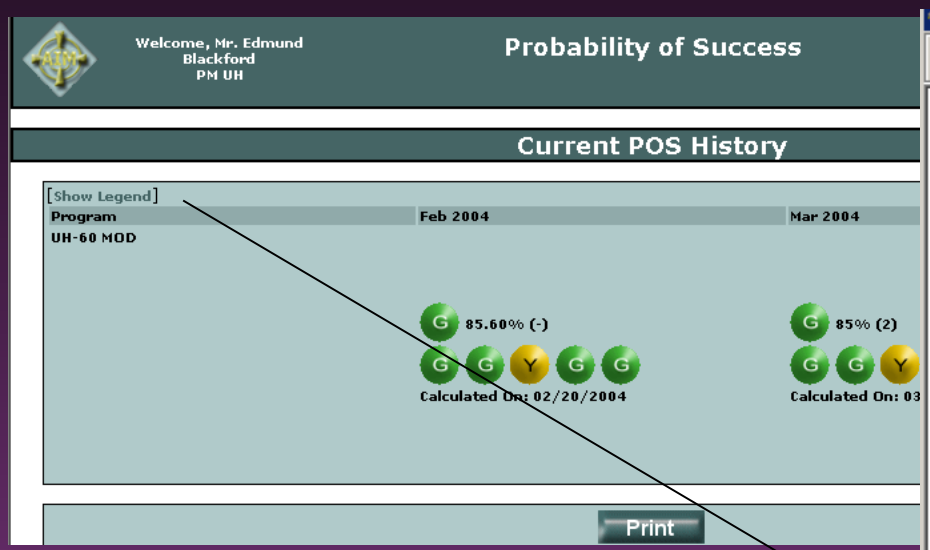

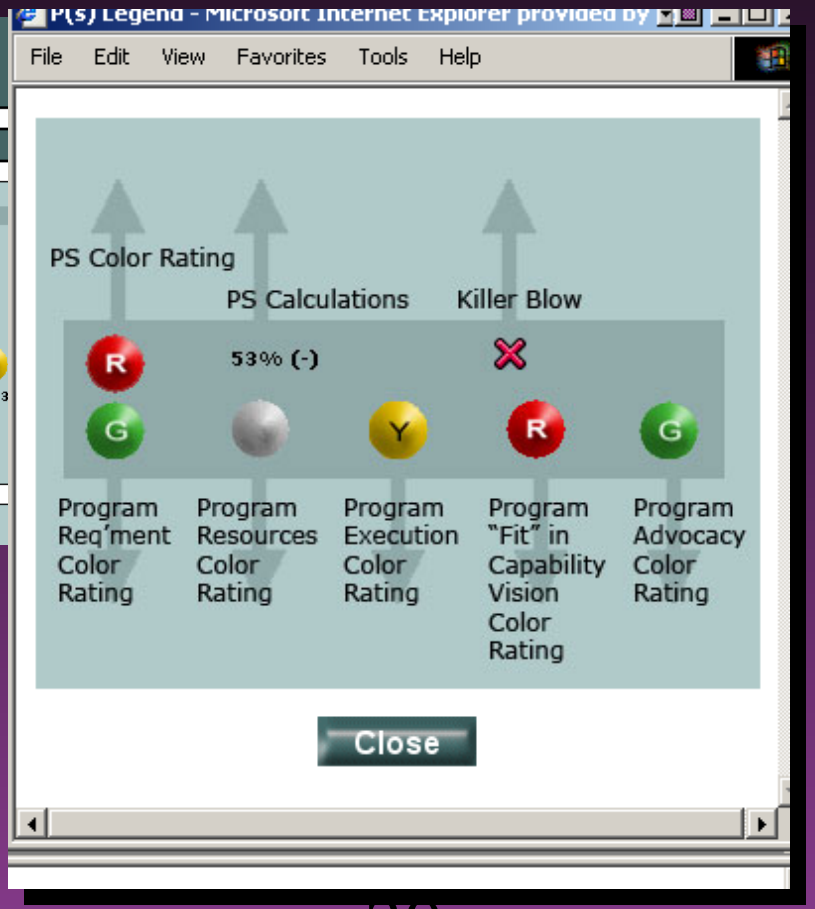

P(S) SummaryReport

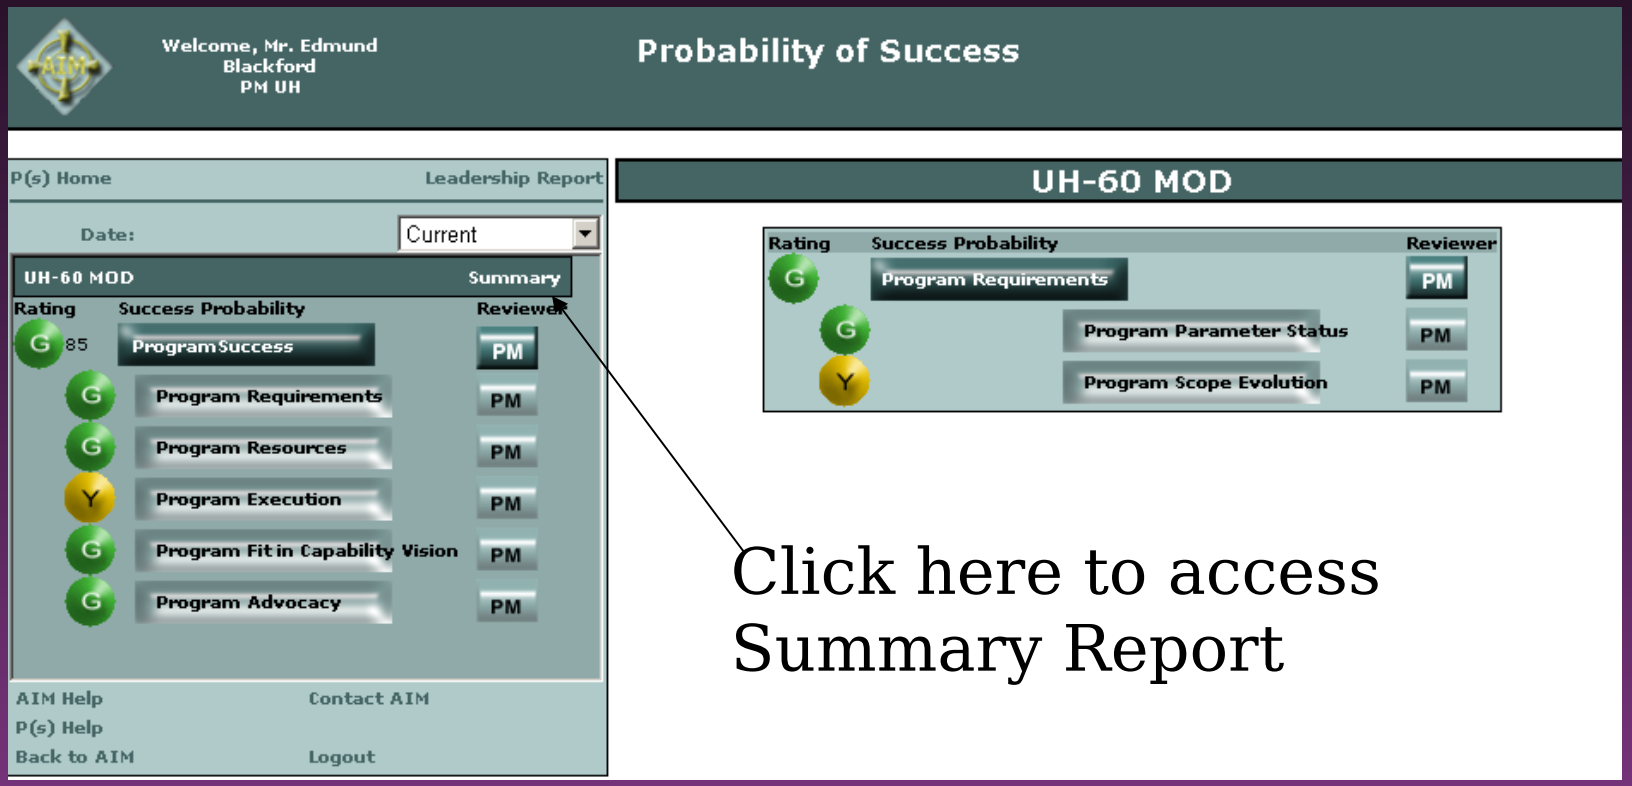

P(S) Summary Report

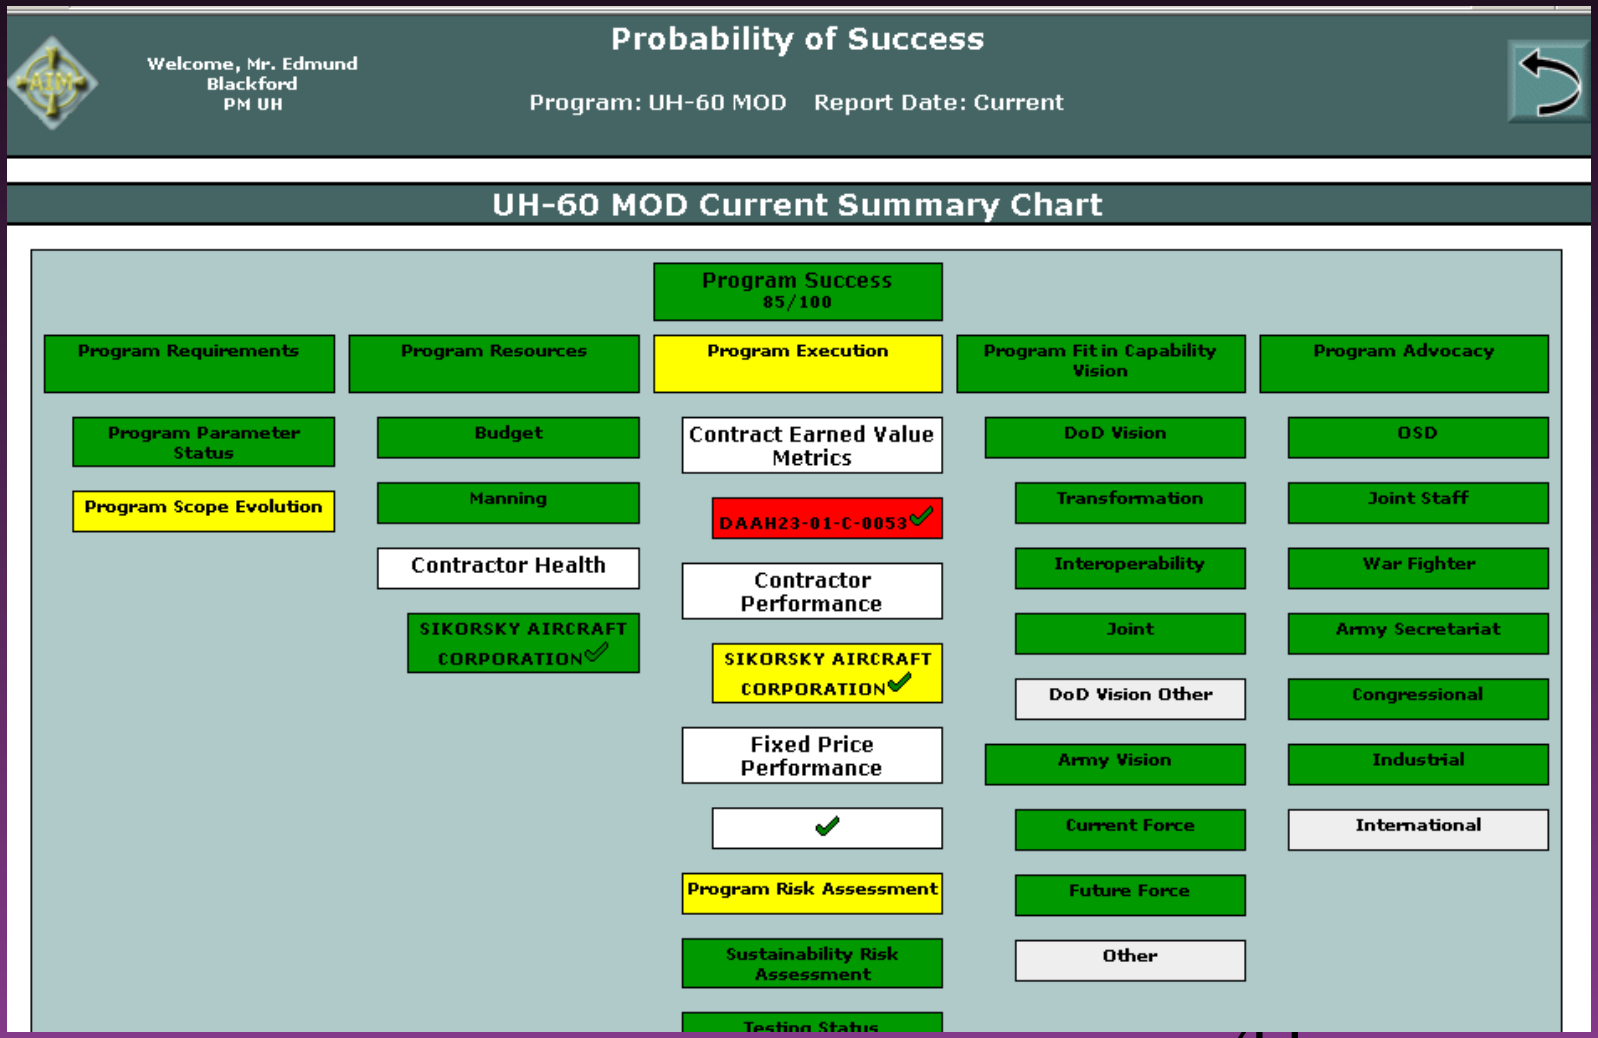

Questions?
